

# Belmont Middle & High School Project Update

March 2022

# Work Performed – March 2022

## **Field House Locker Room Renovation**

- Completed insulating plumbing
- Completed electrical and plumbing inspections
- Completed installation of drywall
- Continued finishing of drywall
- Continue misc. masonry restoration
- Started installation of plumbing fixtures
- Started installation of HVAC 1 unit

## **Phase 2 Site Work and Utilities**

- Continued installation of phase 2 utilities
  - Completed site utilities at North Road
  - Continued installation of under-slab utilities
  - Started installation of North Road sub-grade
- Continued installation of retaining wall
- Started installation of retention system

## **Phase 2 Structure**

- Completed erection of structural steel for Areas D and F
  - Complete F wing steel erection
- Completed decking and detailing Areas D and F
- Completed preparing for Area D slabs on metal deck
- Completed placing slabs on deck in Area D
- Started preparing for Area F slabs on metal deck
- Started preparing for Area D slab on grade
- Started spray fireproofing Area D structure

## **Phase 2 Interiors**

- Continued installation of Radiant Piping
- Started layout and top track for Area D interior partitions

## **Phase 1**

- Continued commissioning and balancing

# Look Ahead – April 2022

## **Field House Locker Room Renovation**

- Complete installation of HVAC 1 unit
- Complete finishing of drywall
- Continue misc. masonry restoration
- Continue installation of plumbing finishes
- Start painting
- Start old boiler room (E111) roof replacement

## **Phase 2 Site Work and Utilities**

- Continue installation of phase 2 utilities
  - Continue installation of North road sub grade
  - Complete installation of under-slab utilities
- Continue installation of retaining wall

## **Phase 2 Structure**

- Complete preparing for Area F slabs on metal deck
- Continue spray fireproofing structure
- Start placing slab on grade in Area D
- Start preparing for Area F slab on grade
- Start framing exterior façade

## **Phase 2 Interiors**

- Continue installation of Radiant Piping
- Continue layout and top track for Area D interior partitions
- Start layout and top track for Area F interior partitions
- Start MEPFP rough-in above ceiling

## **Phase 1**

- Continue commissioning and balancing
- Complete April Break Punch List / Issues List

# Progress Photos

- HVAC 1 in Boys Teams Locker Room



- Drywall and Tape





# Progress Photos – Area F Framing





# Progress Photos

- Underground Plumbing in Area F



- Retention System





# Progress Photos

- Installation of Radiant Piping



- Spray Fireproofing and SOG Rebar






# Progress Photos

- Layout for Interior Partitions



- Wet Cure D2 Slab

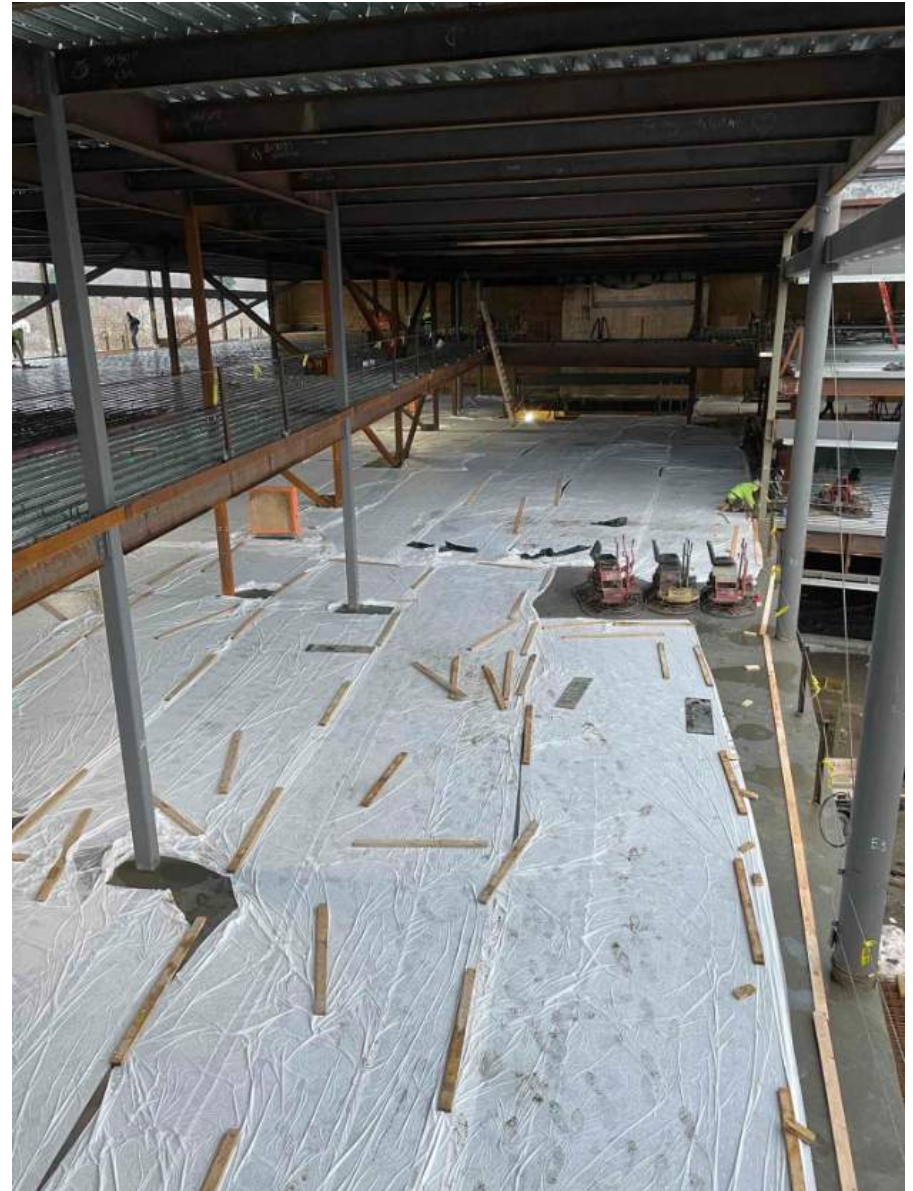



# Progress Photos

