


Activity ID	Activity Name	Remaining Duration	Start	Finish	2021												2022												2023												2024	
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb

Belmont Middle & High School -28Apr21 Schedule Update

Construction Summary

Phase 1 - Construct New School (Partial)

SUM-3170	Abate & Restore Area at Locker Rooms	0	20-Dec-18 A	31-Dec-18 A
Phase 1 - Construct New School (Partial)				
SUM-3180	Bid & Award - Curtain Wall Design Assist	0	20-Mar-19 A	17-Jul-19 A
SUM-3160	Abate, Install Temp Structural for Phasing, Cut Cap, Demo Pool &	0	10-Jun-19 A	30-Aug-19 A
SUM-3250	Begin Mobilization	0	17-Jun-19 A	
SUM-3130	Enabling Site Utilities & New Access Roadway	0	17-Jun-19 A	27-Aug-19 A
SUM-3140	Relocate Utilities at Building Footprint	0	08-Jul-19 A	15-Nov-19 A
SUM-3150	Mobilize Pile Operation & Perform Load Test	0	19-Aug-19 A	11-Sep-19 A
SUM-2000	Install Piles	0	27-Aug-19 A	26-Sep-19 A
SUM-3210	Substantial Completion of Early Bid Package #2 Summer 2019 V	0		30-Aug-19 A
SUM- 2010	FRP Pile Caps & Grade Beams	0	16-Oct-19 A	24-Feb-20 A
SUM- 2020	Structural Steel Erection	0	15-Jan-20 A	15-May-20 A
SUM- 2030	Structural Steel Deck & Detailing	0	20-Jan-20 A	04-Jun-20 A
SUM- 2110	Install Final Site Utilities & Geothermal Wells	0	03-Feb-20 A	23-Sep-20 A
SUM-3270	Complete Foundations	0		24-Feb-20 A
SUM- 2140	Prep & Place Slabs on Deck	0	18-Mar-20 A	08-Jul-20 A
SUM-3190	Shop Drawings Approved - Curtain Wall	0		20-Mar-20 A
SUM- 2150	Layout & Install Top Track	0	28-Apr-20 A	19-Nov-20 A
SUM-3260	Complete Steel Erection	0		15-May-20 A
SUM- 2090	Underslab Utilities / Structural SOG	0	18-May-20 A	16-Nov-20 A
SUM- 2160	Spray Fireproof Steel	0	18-May-20 A	30-Nov-20 A
SUM- 2040	Frame Exterior Walls	0	01-Jun-20 A	30-Nov-20 A
SUM- 2070	Overhead MEP Installation	8	02-Jun-20 A	07-May-21
SUM-1010	Summer Renovations 2020	0	18-Jun-20 A	26-Aug-20 A
SUM- 2170	Sheath Exterior Walls	0	24-Jun-20 A	18-Dec-20 A
SUM- 2180	AVB Exterior Walls	0	26-Jun-20 A	24-Feb-21 A
SUM-3295	Complete Slabs on Deck	0		08-Jul-20 A
SUM- 2050	Install Roof Sheathing & AVB	35	08-Jul-20 A	16-Jun-21
SUM-3200	Begin - Curtain Wall	0	20-Jul-20 A	
SUM- 2210	Install Curtain Wall	31	20-Jul-20 A	10-Jun-21
SUM- 2190	Install Brick	8	03-Aug-20 A	07-May-21
SUM- 2130	Install Final Site Work	75	08-Sep-20 A	11-Aug-21
SUM- 2080	Install Drywall & Finishes	87	29-Sep-20 A	27-Aug-21
MILE- 2070	Building Tight - Area A	0		06-Oct-20 A
SUM-3300	Complete Spray Fireproofing	0		30-Nov-20 A
MILE- 2080	Building Tight - Area B	0		01-Dec-20 A
SUM- 2200	Install Metal Panels	0	23-Dec-20 A	20-Apr-21 A
MILE- 2090	Building Tight - Area CD	0		31-Dec-20 A
MILE-2080	Begin Equipment Start-up	0	07-May-21	
SUM- 2120	Install Playing Field (North End of Site)	64	17-May-21	13-Aug-21
SUM-3230	Summer Renovations 2021	51	24-Jun-21	02-Sep-21
MILE-2090	Receive Temporary Certificate of Occupancy for High School	0		24-Aug-21
SUM-2135	Students / Staff Occupy New School	10	25-Aug-21	08-Sep-21
SUM- 2100	Install Playing Field (Western End of Site)	34	01-Sep-22	20-Oct-22
Phase 2 - Demo Remaining School / Complete School				
SUM-3360	Begin Mobilization	0	28-Jun-21	
SUM-3000	Mobilize for Phase 2 Construction	13	28-Jun-21	14-Jul-21
SUM-3010	Complete Abatement & Demo of Existing Building	180	15-Jul-21	01-Apr-22
SUM-3350	Begin Piles	0	15-Dec-21	
SUM-3030	Pile Installation	20	15-Dec-21	13-Jan-22
SUM-3040	Concrete Foundations	45	14-Jan-22	18-Mar-22
SUM-3310	Complete Foundations	0		18-Mar-22
SUM-3050	Structural Steel Erection	40	28-Mar-22	23-May-22
SUM-3060	Install Decking / Detail	58	05-Apr-22	27-Jun-22
SUM-3220	Prep & Place Slabs on Deck	43	04-May-22	05-Jul-22
SUM-3320	Complete Steel Erection	0		23-May-22

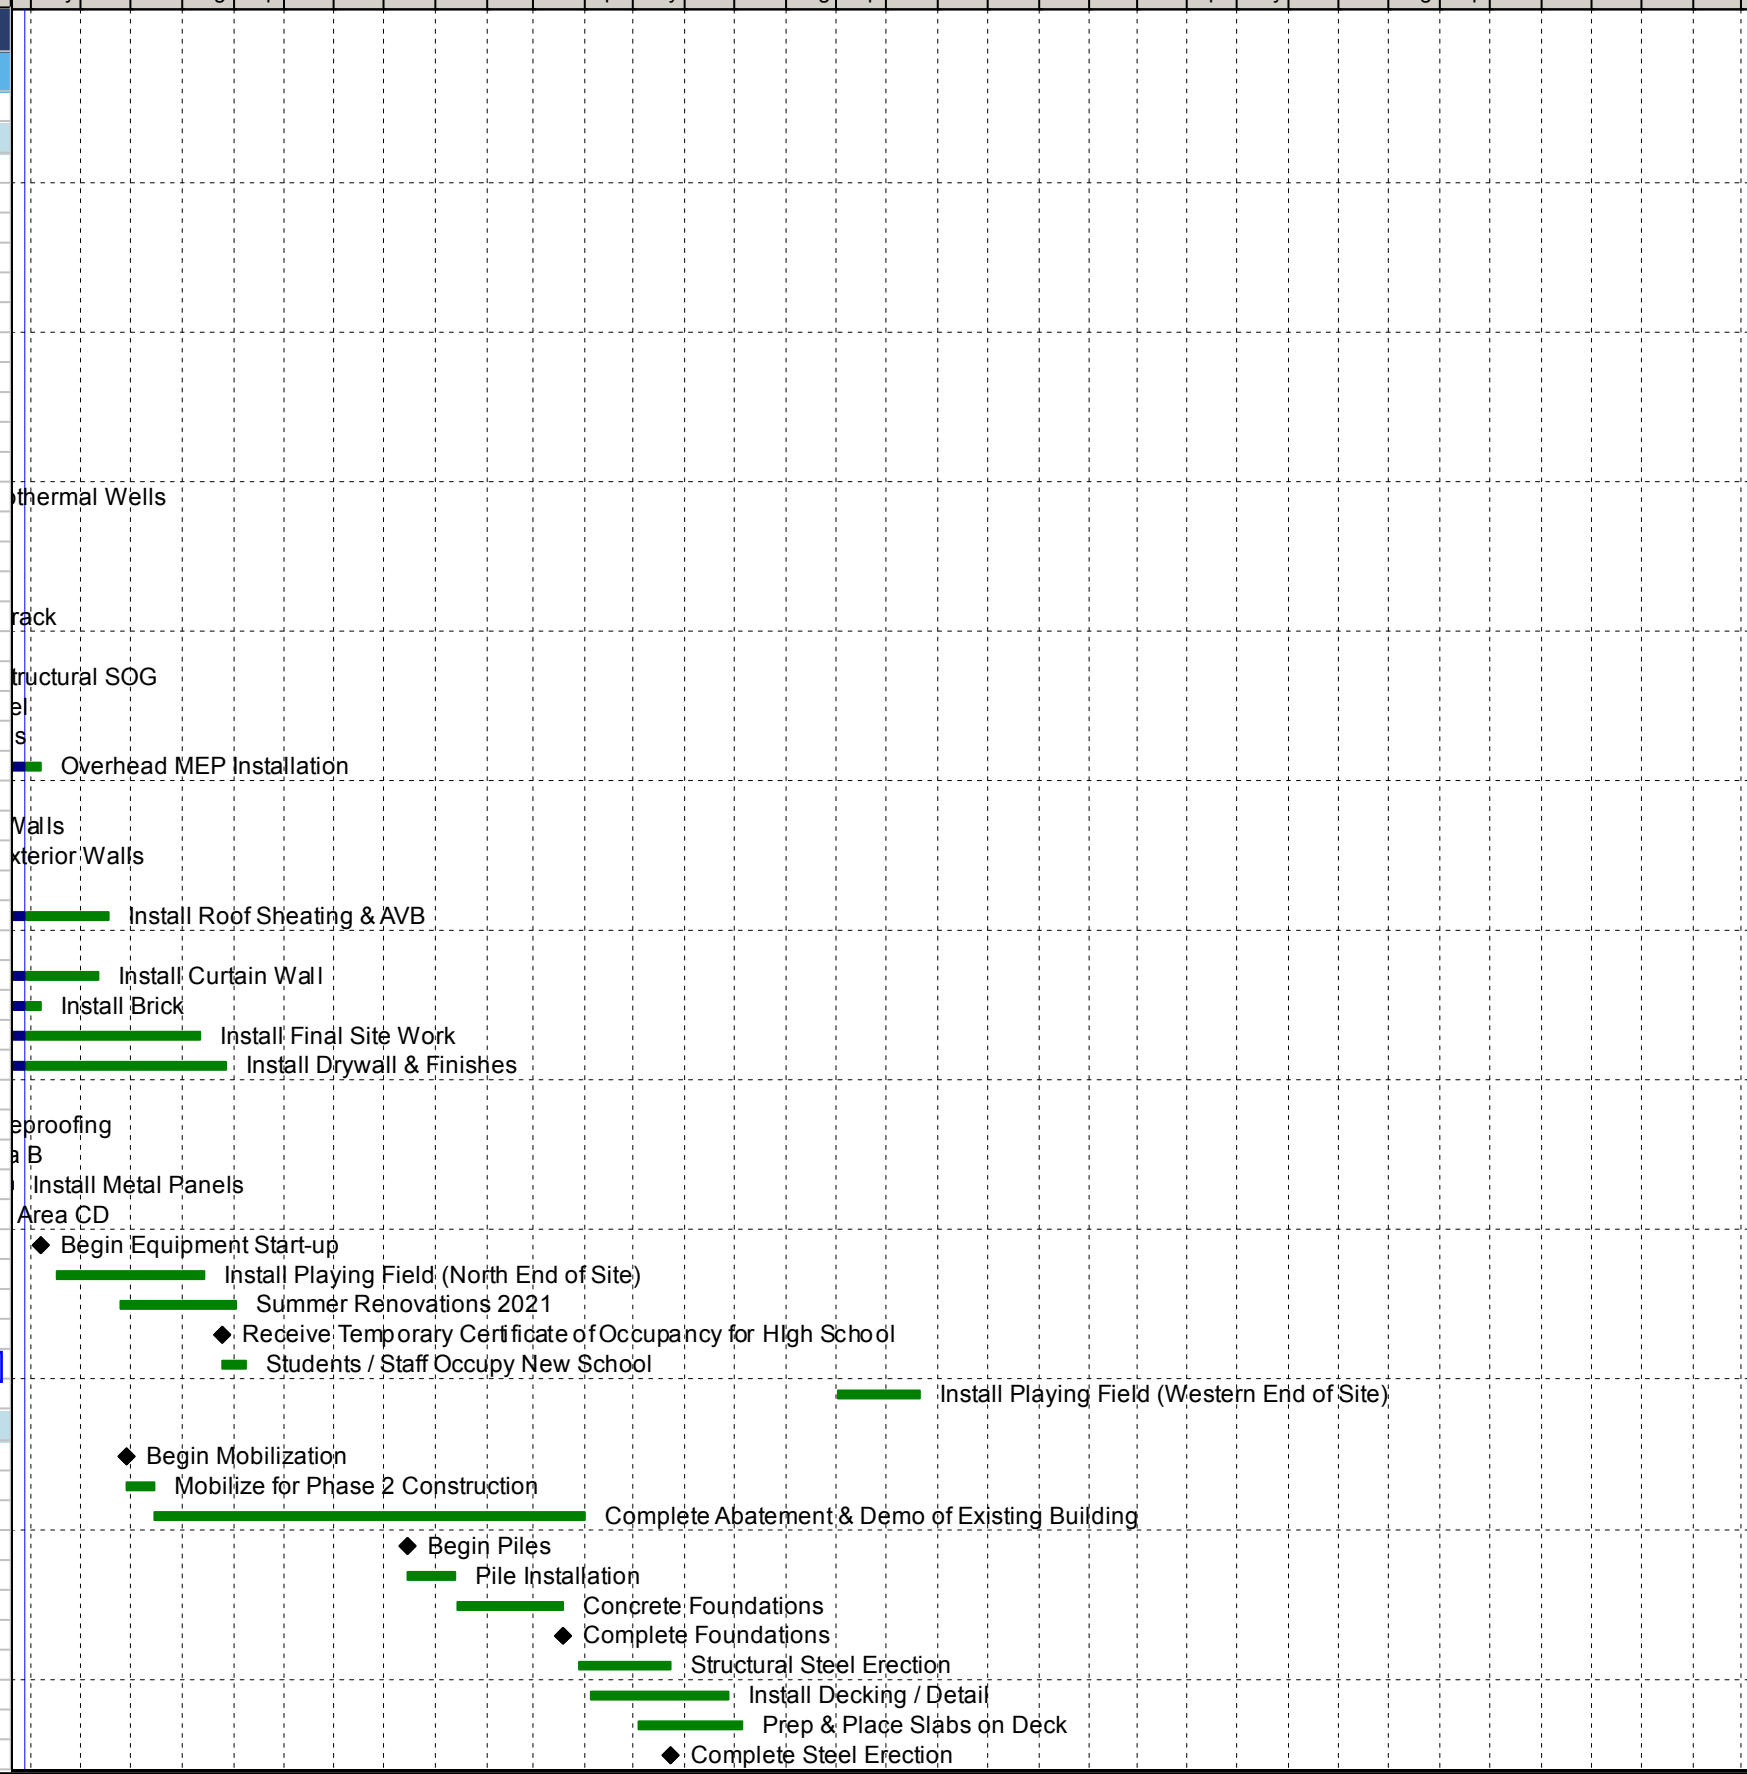

Remaining Level of Effort	Remaining Work
Actual Level of Effort	Critical Remaining Work
Actual Work	Milestone



