

Belmont Middle & High School Project Update

February 2023

Work Performed – February 2023

Phase 1

- February work-to-complete list

Phase 2 Site Work and Utilities

- Completed PH2 Site Lighting
- Installing sidewalks on hold due to winter condition
- Raising grade via existing material on hold due to winter condition
- Final grading athletic fields on hold due to winter condition
- Installing drainage at athletic fields on hold due to winter condition

Phase 2 Interiors

- Phase 2 elevator ready for testing
- Started balancing HVAC system
- Continued installation of floor tile on Level 1
- Started up HRU's and AC units
- Started testing Fire Alarm

Area D

- Continued flooding ACT ceiling tiles
- Completed finishing ACT-14 ceilings
- Continued installation of wall tile
- Continued installation of plinth at Stair 4
- Continued installation of PLAM windowsills
- Started sealing concrete floors in Art rooms

○ Area F

- Started installation of wall tile on Level 1
- Started flooding ACT ceilings on Levels 2 & 3
- Completed framing ACT ceilings on Level 1
- Continued installation of light fixtures
- Completed installation of casework
- Completed installation of linoleum flooring

Look Ahead – March 2023

Phase 1

- Continue commissioning and balancing
- Continue general work to complete list

Phase 2 Site Work and Utilities

- Continue raising grade via existing material
- Continue final grading athletic fields
- Continue installing drainage for athletic fields
- Continue installation of sidewalks

Phase 2

- Continue balancing HVAC System
- Complete Floor Tile install on Level 1
- Phase 2 Elevator ready for testing
- Complete start up of all Phase 2 equipment
- Start Punch List

Area D

- Complete flooding ACT ceilings
- Complete installing wall tile
- Complete installation of plinth at Stair 4
- Complete installation of PLAM windowsills
- Complete sealed concrete in Art rooms

Area F

- Complete installing wall tile
- Complete flooding ACT ceilings

Progress Photos

Area D Level 2




Progress Photos

Area D Level 2 Media Center



Progress Photos

Stair 4 Plinth and Area F Level 1 Corridor

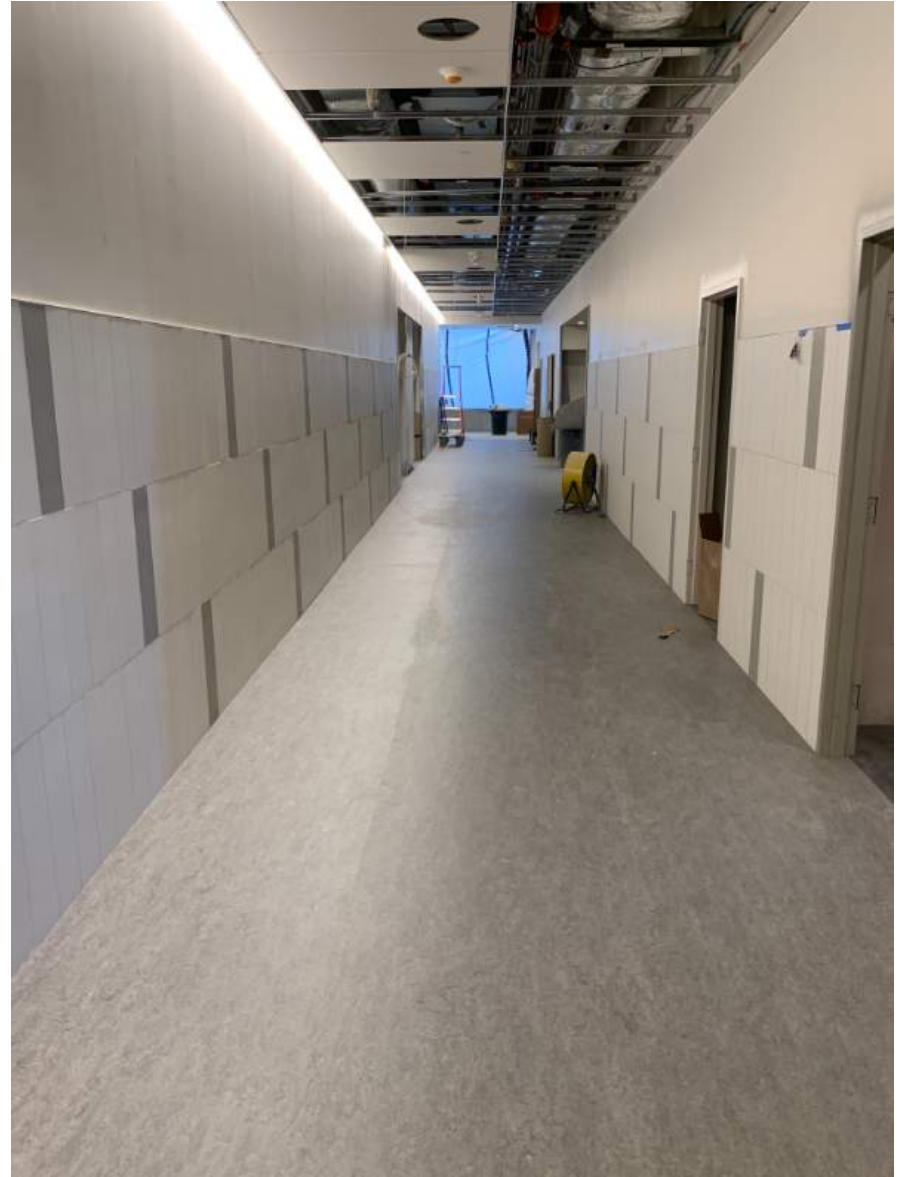

Progress Photos

Area D Level 1 Art Room



Progress Photos



Area D Level 1 Corridor

