

Belmont Middle & High School Project Update

March 2023

Work Performed – March 2023

Phase 1

- Geothermal flushing operation

Phase 2 Site Work and Utilities

- Continued installing sidewalks
- Continued raising grade via existing material
- Continued final grading athletic fields
- Continued installing drainage at athletic fields

Phase 2 Interiors

- Phase 2 elevator ready for testing
- Continued balancing HVAC system
- Started up all Phase 2 equipment

Area D

- Completed flooding ACT ceiling tiles
- Completed installation of wall tile
- Continued installation of plinth at Stair 4
- Completed installation of PLAM windowsills
- Completed sealing concrete floors in Art rooms
- Started installing rubber base
- Started installing carpet tile
- Started Punch List

○ Area F

- Completed installation of wall tile on Level 1
- Completed flooding ACT ceilings on Levels 2 & 3
- Completed installation of light fixtures
- Started flooding ACT ceiling tiles on Level 1
- Started installing rubber base
- Started Punch List

Look Ahead – April 2023

Phase 1

- Complete April Break work-to-complete list

Phase 2 Site Work and Utilities

- Continue raising grade via existing material
- Continue final grading athletic fields
- Continue installing drainage for athletic fields
- Continue installation of sidewalks

Phase 2

- Complete balancing HVAC System
- Phase 2 Elevator ready for testing
- Start Commissioning

Area D

- Complete installation of plinth at Stair 4
- Complete installation of rubber base
- Complete installation of carpet tile
- Continue Punch List
- Start final cleaning

Area F

- Complete installing rubber base
- Complete flooding ACT ceiling tile on Level 1
- Continue Punch List
- Start final cleaning

Progress Photos

Administration Break Room




Progress Photos

Area D Level 2 Media Center




Progress Photos

Area D Level 2 Media Center

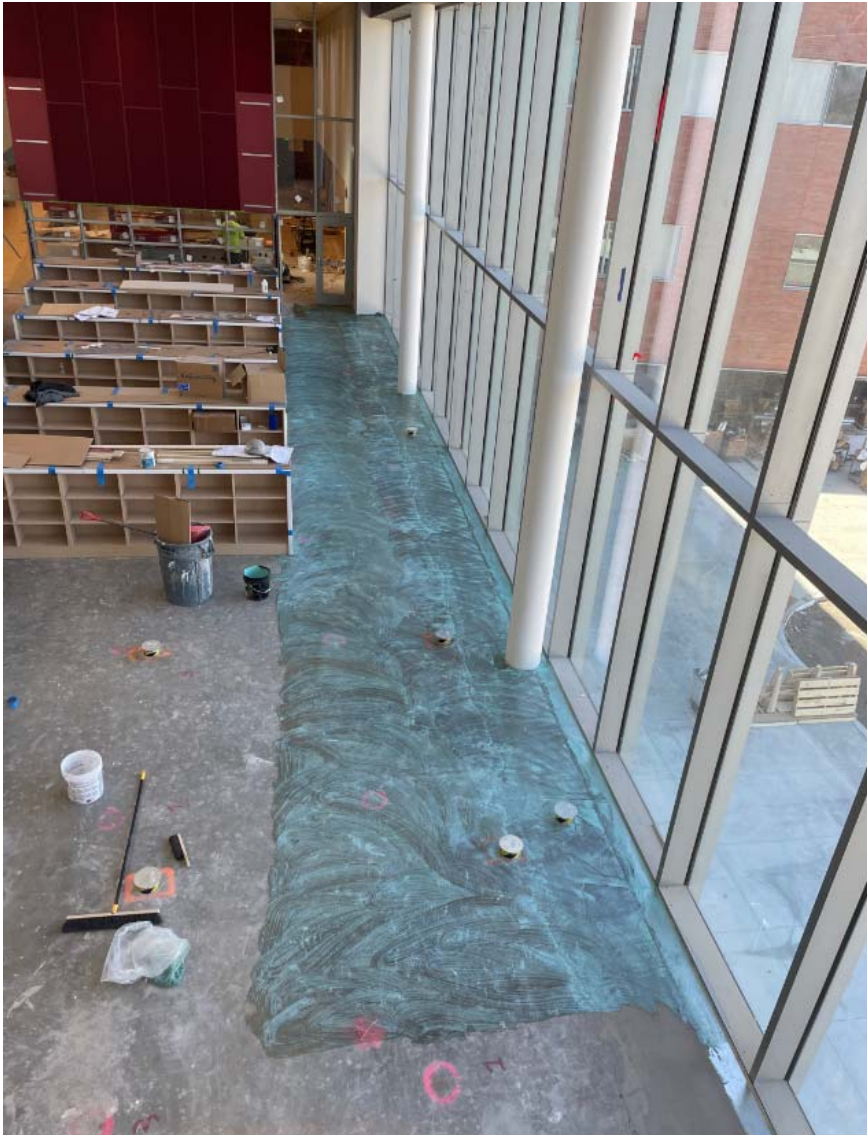

Area D Level 2 Corridor

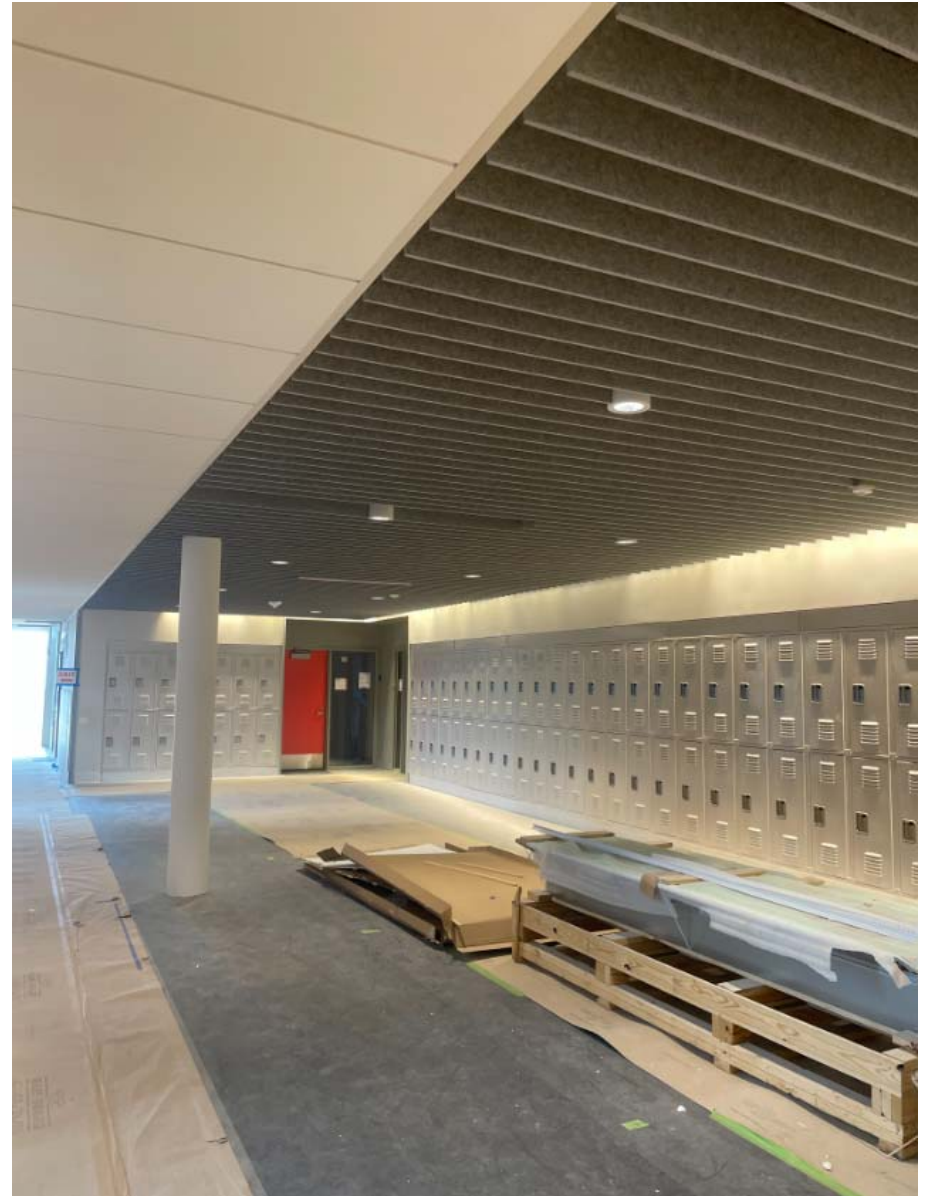

Progress Photos

Art Classroom



Progress Photos

Area F Level 3 Teacher Planning Room



Progress Photos

PH 2 Field Development

