

Belmont Middle & High School Project Update

November 2021

Work Performed – November 2021

Phase 1

- Completed drainage for turf field
- Auditorium
 - Completed installation of wood paneling in Auditorium
 - Completed installation of carpet flooring in Auditorium
 - Completed installation of wood flooring system on stage
 - Completed installation of fire curtain at stage
 - Continued installation of stage equipment in Auditorium
 - Started punch list in auditorium
- Continued punch list on 2nd shift
- Continued start-up, testing and balancing of HVAC systems
- Started installing synthetic turf field system

Phase 2

- Continued installation of mini piles
- Continued installation of phase 2 utilities
- Continued renovation of Field House Locker Rooms
 - Completed drilling and dowelling existing slab
 - Started installation of topping slab
- Continued prepping piles for pile caps
- Continued prepping for segmented retaining wall installation
- Started installation of rebar and pouring concrete for pile caps / grade beams
 - Started cold weather mitigation for concrete
- Started site preparations for generator pad

Look Ahead – December 2021

Phase 1

- Continue punch list on 2nd shift
- Continue start-up, testing and balancing of HVAC systems
- Continue Installation of stage equipment
- Continue synthetic turf installation

Phase 2

- Continue installation of phase 2 utilities
- Continue renovation of Field House Locker Rooms
- Continue installing rebar and pouring pile caps and grade beams
- Start construction of segmented retaining wall
- Complete site preparations at generator pad
- Install generator


Progress Photos

- Installation of Theater Rigging




Progress Photos

- Stage Floor and Fire Curtain

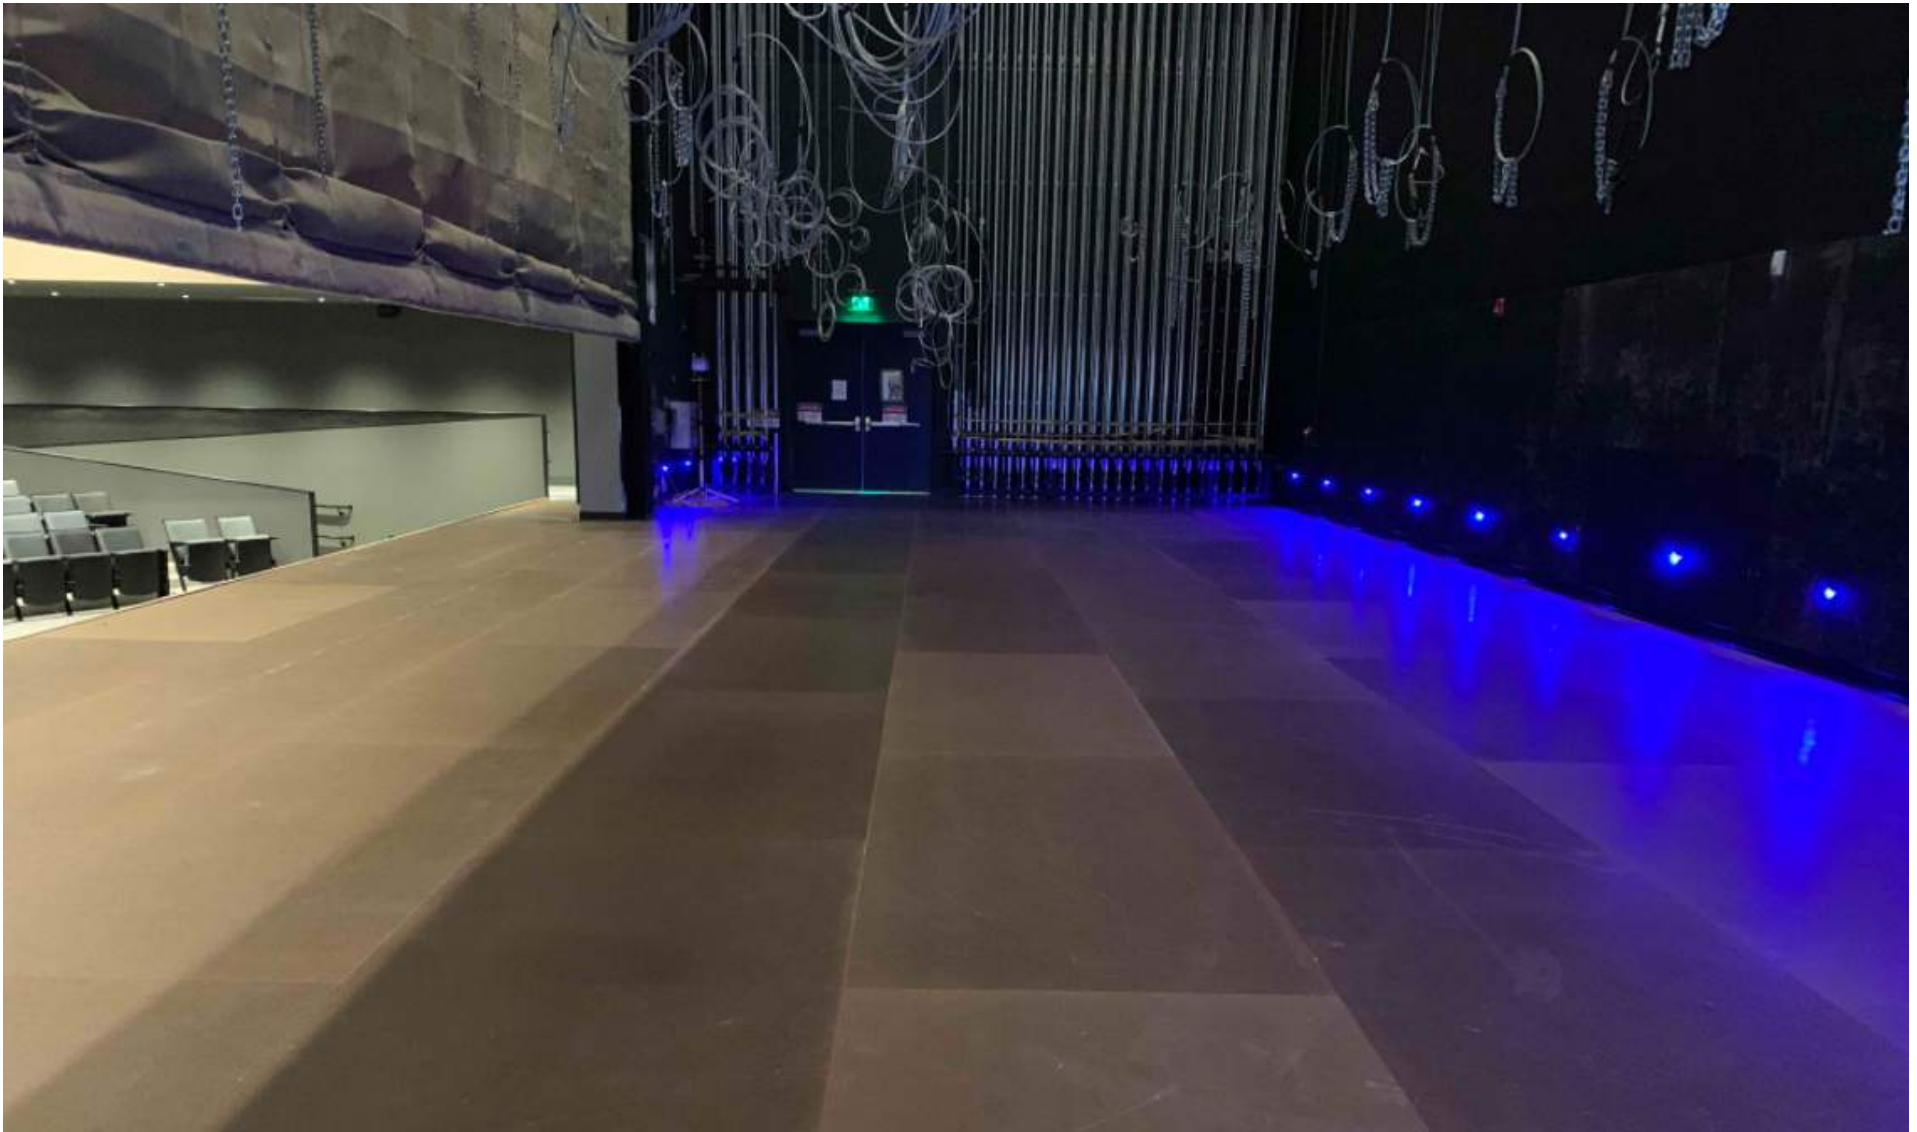

Progress Photos

- Rugby / Football Field Drainage

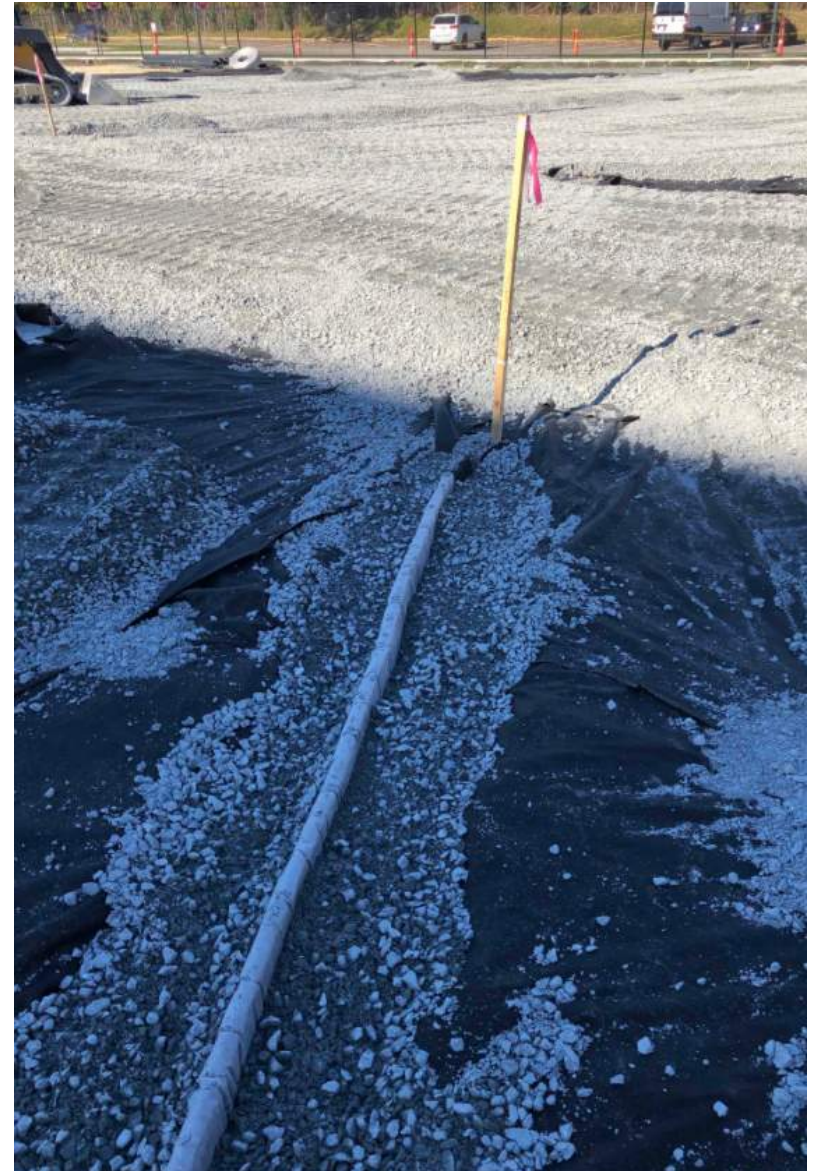

Progress Photos

- Installation of Synthetic Turf



Progress Photos

– Installation of Synthetic Turf



Progress Photos – Locker Room Renovation Plumbing and Slab Prep



Progress Photos

– Locker Room Renovation Slab Prep



Progress Photos

- Locker Room Renovation Topping Slab



Progress Photos

– Phase 2 Foundations



Progress Photos

- Area D Grade Beam and Pile Cap Rebar



Progress Photos

- Underground Utilities and Formwork Installation



Progress Photos

– Area D Grade Beam and Pile Cap Concrete and Formwork



Progress Photos

– Generator Pad Formwork

