

# Belmont Middle & High School Project Update

December 2021

# Work Performed – December 2021

## Phase 1

- Completed installing synthetic turf field system
- Auditorium
  - Continued installation of stage equipment in Auditorium
  - Continued punch list in auditorium
- Continued punch list on 2<sup>nd</sup> shift
- Continued start-up, testing and balancing of HVAC systems
- Completed miscellaneous work during winter break within occupied phase 1 building

## Phase 2

- Completed installation of mini piles
- Completed prepping piles for pile caps
- Completed installation of rebar and pouring concrete for pile caps / grade beams
  - Continued cold weather mitigation for concrete
- Continued installation of phase 2 utilities
- Continued renovation of Field House Locker Rooms
  - Completed installation of topping slab
  - Started installing interior wall framing
  - Started installing above ceiling and in-wall MEPFP's
- Continued installation and startup of generator
  - Completed installation of generator pad
  - Completed setting generator
  - Started cutting over generator into emergency power systems
- Started erection of structural steel for Areas D and F

# Look Ahead – January 2022

## Phase 1

- Complete punch list on 2<sup>nd</sup> shift until Summer '22
- Complete start-up, testing and balancing of HVAC systems until Summer '22
- Complete Installation of stage equipment

## Phase 2

- Continue installation of phase 2 utilities
- Continue renovation of Field House Locker Rooms
- Continue renovation of Field House Locker Rooms
  - Continue installing interior wall framing
  - Continue installing above ceiling and in-wall MEPFP's
- Start erection of structural steel for Areas D and F
- Start decking and detailing area D and F
- Continue retaining wall at north side of site

# Progress Photos

- Pouring Grade Beam at Area D





# Progress Photos

- Backfilling Grade Beam at Area D





# Progress Photos

- Installation of Underground Plumbing Utilites





# Progress Photos

– Steel Erection



# Progress Photos

- Installation of interior walls and plumbing in Locker Rooms






# Progress Photos

- Re-Installation of Interior Glazing During Winter Break



- Installation of Stage Rigging

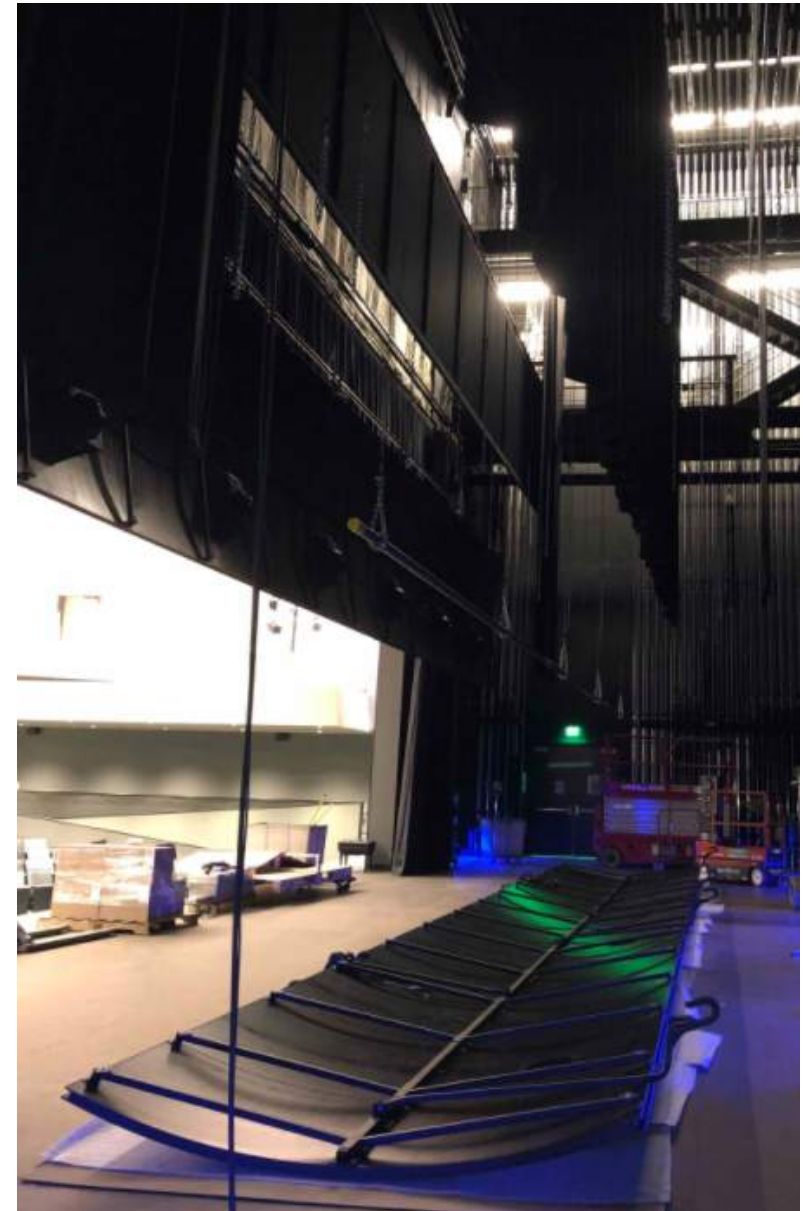

# Progress Photos

- Installation of Acoustical Wall Panels and Wenger Cabinets in Music Rooms

