

Belmont Middle & High School Project Update

January 2022

Work Performed – January 2022

Phase 1

- Substantially Completed Auditorium and Stage Rigging
- Completed punch list on 2nd shift until Summer '22
- Completed start-up, testing and balancing of HVAC systems
- Continued commissioning of HVAC systems

Phase 2

- Continued phase 2 site utility work
 - Completed installation of primary electrical duct bank
 - Installed drainage structures throughout fields
- Continued renovation of Field House Locker Rooms
 - Completed installation of above ceiling and in-wall MEPFP's rough-in
 - Completed installing interior wall framing
 - Started installing in-wall blocking
 - Started installing drywall
- Started erection of structural steel for Areas D
 - Completed erection of Batch 1
 - Started erection of Batch 2
- Started installation of steel decking and detailing for Batch 1

Look Ahead – February 2022

Phase 1

- February Break Work to Complete
 - Install misc. casework items
 - Complete casework punch list
 - Complete PA system cutover with Belmont Light
 - Install motorized shades
 - Expose steel connections at Phasing wall for Phase 2 tie-in
 - Continue troubleshooting lighting controls
 - Cutover permanent generator

Phase 2

- Continue installation of phase 2 utilities
- Continue installation of retaining wall
- Continue renovation of Field House Locker Rooms
 - Complete installation of in-wall blocking
 - Continue installation of drywall
- Continue erection of structural steel for Areas D and F
 - Complete D wing steel erection
 - Start F wing steel erection
- Continue decking and detailing Areas D and F
- Start preparing Area D slabs on metal deck

Progress Photos

- Primary Electrical Duct Bank along North side of site




Progress Photos

- Locker Room Renovation



Progress Photos

– Boiler Room to Locker Room Renovation

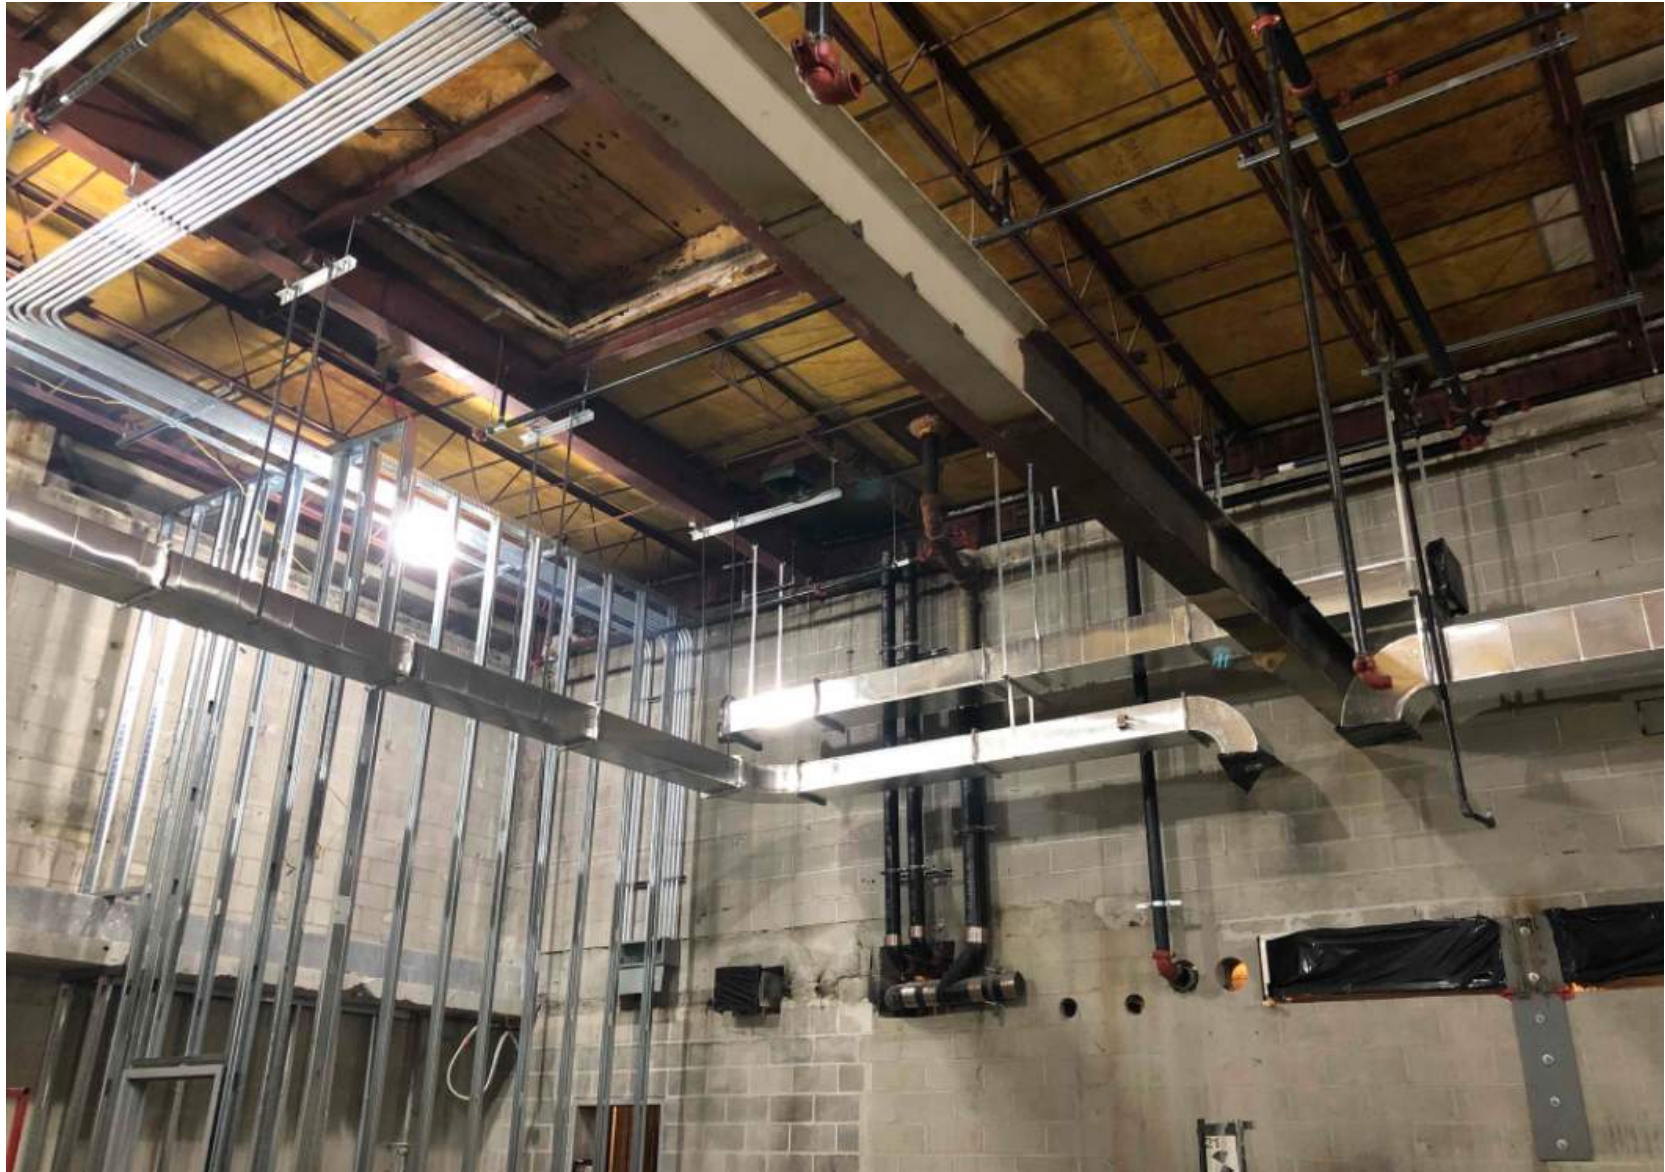

Progress Photos

- Installation steel decking



Progress Photos

– Steel Erection



Progress Photos

– Steel Erection

