

Belmont Middle & High School Project Update

February 2022



Work Performed – February 2022

Phase 1

- Continued commissioning of HVAC systems
- Completed Misc. Work in the High School over February Break
 - Connected phasing steel to high school in E100A
 - Installed shelving in D489
 - Installed casework in B143
 - Installed shades in Cafeteria
 - Installed batting cages in Field House
 - Installed missing room signage
 - Installed missing security cameras
 - Completed testing of lockdown system
 - Worked on misc. punch list items throughout building

Phase 2

- Continued phase 2 site utility work
- Continued renovation of Field House Locker Rooms
 - Completed installation of steel supports for HVAC units
 - Completed installing in-wall blocking
 - Continued installing drywall
 - Started misc. masonry restoration
 - Started insulating plumbing
- Continued erection of structural steel for Areas D & F
 - Completed erection of Batches 2, 3, 4
 - Started erection of Batch 5
- Continued installation of steel decking and detailing
 - Turned over Area D, Levels 2, 3, and 4
 - Started decking and detailing Area F
- Started prepping for concrete slabs on metal deck

Look Ahead – March 2022

Field House Locker Room Renovation

- Complete insulating plumbing
- Complete electrical and plumbing inspections
- Complete installation of drywall
- Complete finishing of drywall
- Continue misc. masonry restoration
- Start painting
- Start installation of plumbing fixtures

Phase 2 Site Work and Utilities

- Continue installation of phase 2 utilities
 - Continue site utilities at North Road
 - Complete installation of under-slab utilities
- Continue installation of retaining wall

Phase 2 Structure

- Continue erection of structural steel for Areas D and F
 - Complete F wing steel erection
- Complete decking and detailing Areas D and F
- Continue preparing for Area D slabs on metal deck
- Start placing slabs on deck in Area D
- Start preparing for Area F slabs on metal deck

Progress Photos

- Areas D and F Steel Erection



Progress Photos

– Area D Decking



Progress Photos

– Area F Framing



Progress Photos

- Drywall Progress in Locker Room




Progress Photos

- Locker Room Shower and Bathroom in-wall



Progress Photos

- Locker Room Masonry Restoration

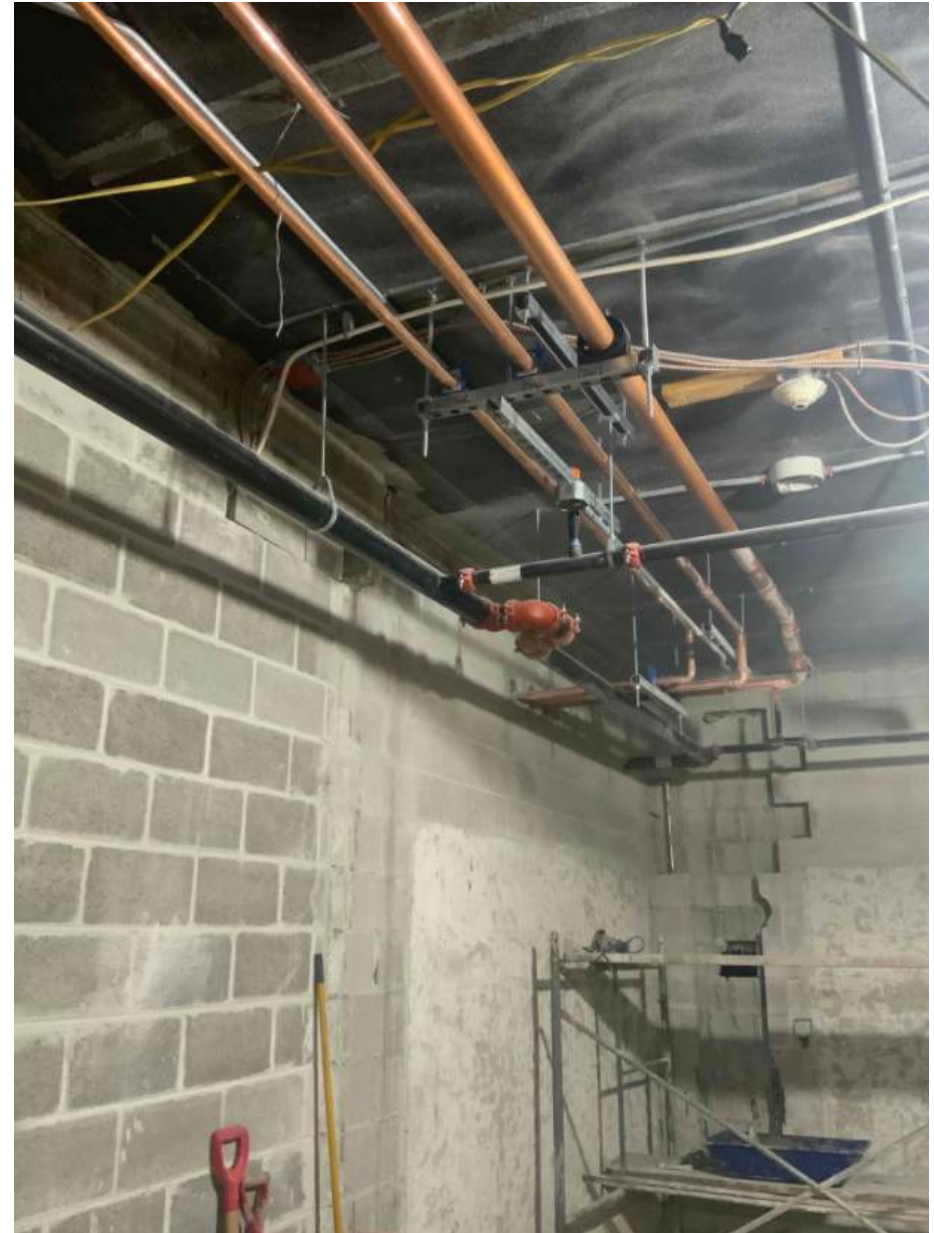


Progress Photos

– Steel Support for HVAC equipment in old boiler room



Progress Photos

– Batting Cages in Field House

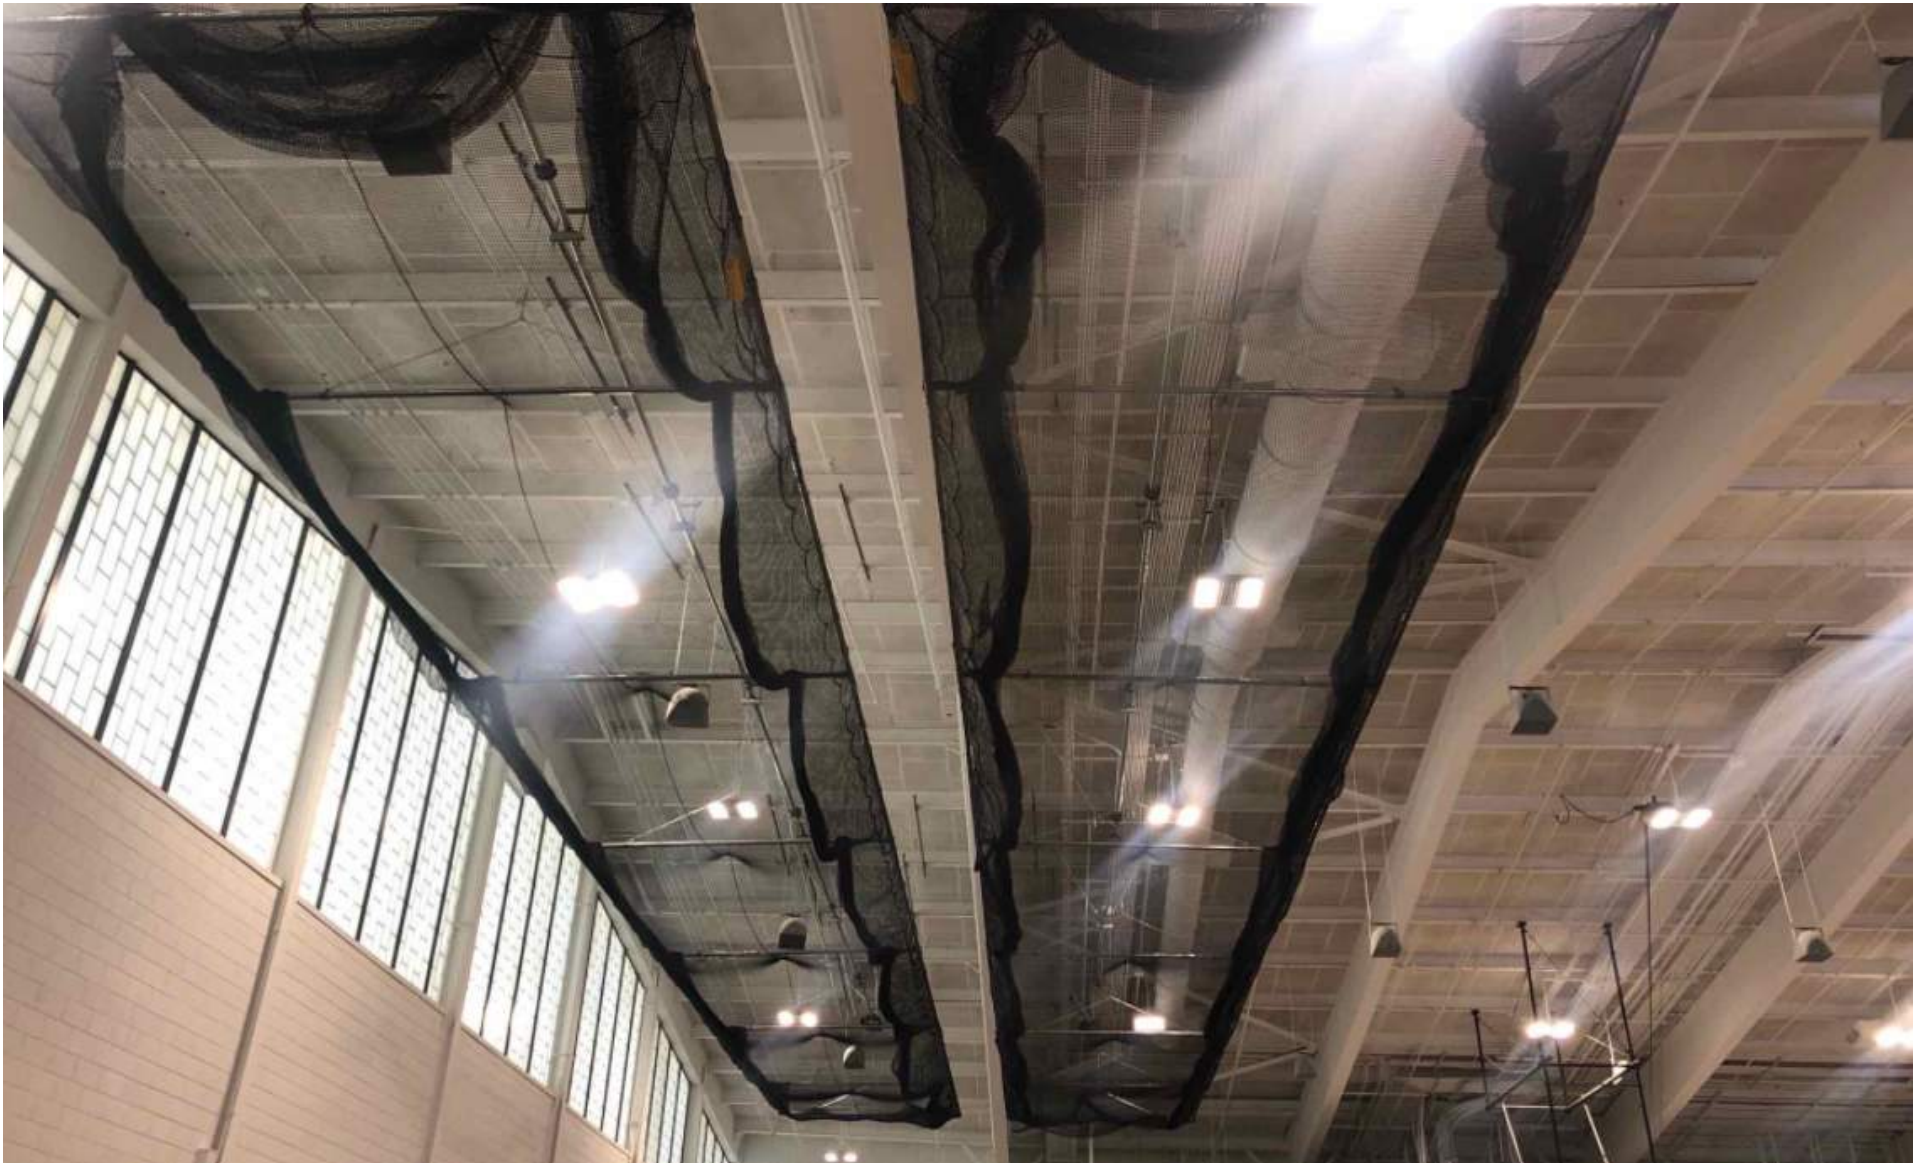

Progress Photos

- Installation of Shelving in Coding Classroom

