

Belmont Middle & High School Project Update

April 2022

Work Performed – April 2022

Field House Locker Room Renovation

- Completed installation of HVAC 1 unit
- Completed installation of Drywall
- Continued misc. masonry restoration
- Continued installation of plumbing fixtures
- Started finishing drywall
- Started interior paint
- Started old boiler room (E111) roof replacement

Phase 2 Site Work and Utilities

- Started reclamation of old parking lot sub grade
- Started raising grade via existing material
- Continued installation of phase 2 utilities
 - Completed installation of under-slab utilities
 - Continued installation of North Road sub-grade
- Completed installation of retaining wall
- Completed installation of retention system

Phase 2 Structure

- Completed preparing for Area F slabs on metal deck
- Completed preparing for Area D slab on grade
- Completed pouring Area F slabs on metal deck
- Continued spray fireproofing Area D structure
- Starting preparing for Area F slab on grade

Phase 2 Interiors

- Completed installation of Radiant Piping on upper floors
- Continued layout and top track for interior partitions
- Started installation of overhead MEPFP's

Phase 2 Exterior

- Started installation of exterior framing
- Started installation of roof parapet

Phase 1

- Continued commissioning and balancing
- Continued Phase 1 work-to-complete during April Vacation

Look Ahead – May 2022

Field House Locker Room Renovation

- Continue misc. masonry restoration
- Continue installation of plumbing finishes
- Continue painting
- Complete old boiler room (E111) roof replacement

Phase 2 Site Work and Utilities

- Continue reclamation of old parking lot sub grade
- Continue raising grade via existing material
- Continue installation of phase 2 utilities
 - Complete installation of North road sub grade

Phase 2 Structure

- Complete spray fireproofing structure
- Complete placing slabs on grade

Phase 2 Interiors

- Continue layout and top track for Area D interior partitions
- Continue layout and top track for Area F interior partitions
- Continue MEPFP rough-in above ceiling
- Start Elevator Core

Phase 2 Exterior

- Complete installation of roof parapet
- Continue installation of exterior framing
- Start installation of roof sheathing and AVB

Phase 1

- Continue commissioning and balancing
- Complete April Break Punch List / Issues List

Progress Photos

- Installation of North Road sub-grade



Progress Photos

- In-slab utilities and support for SOG Area D




- SOD prep for F-Wing Roof



Progress Photos

– Installation of interior Framing and above-ceiling MEP/FP's

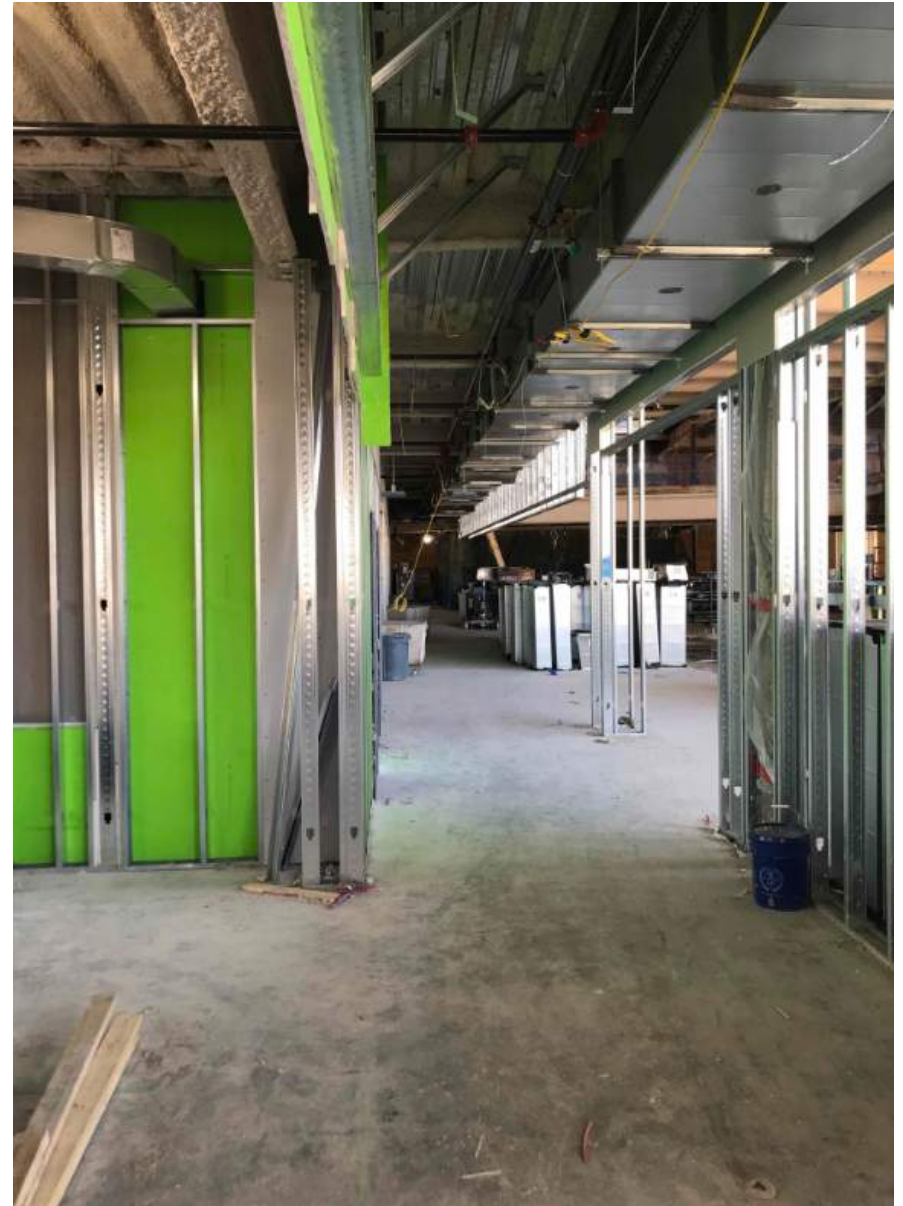

Progress Photos

- Installation of under-slab utilities Area F



- Installation of interior Framing and above-ceiling MEP/FP's




Progress Photos

- Slab on Deck Placement Area D



- Installation of Roof parapet

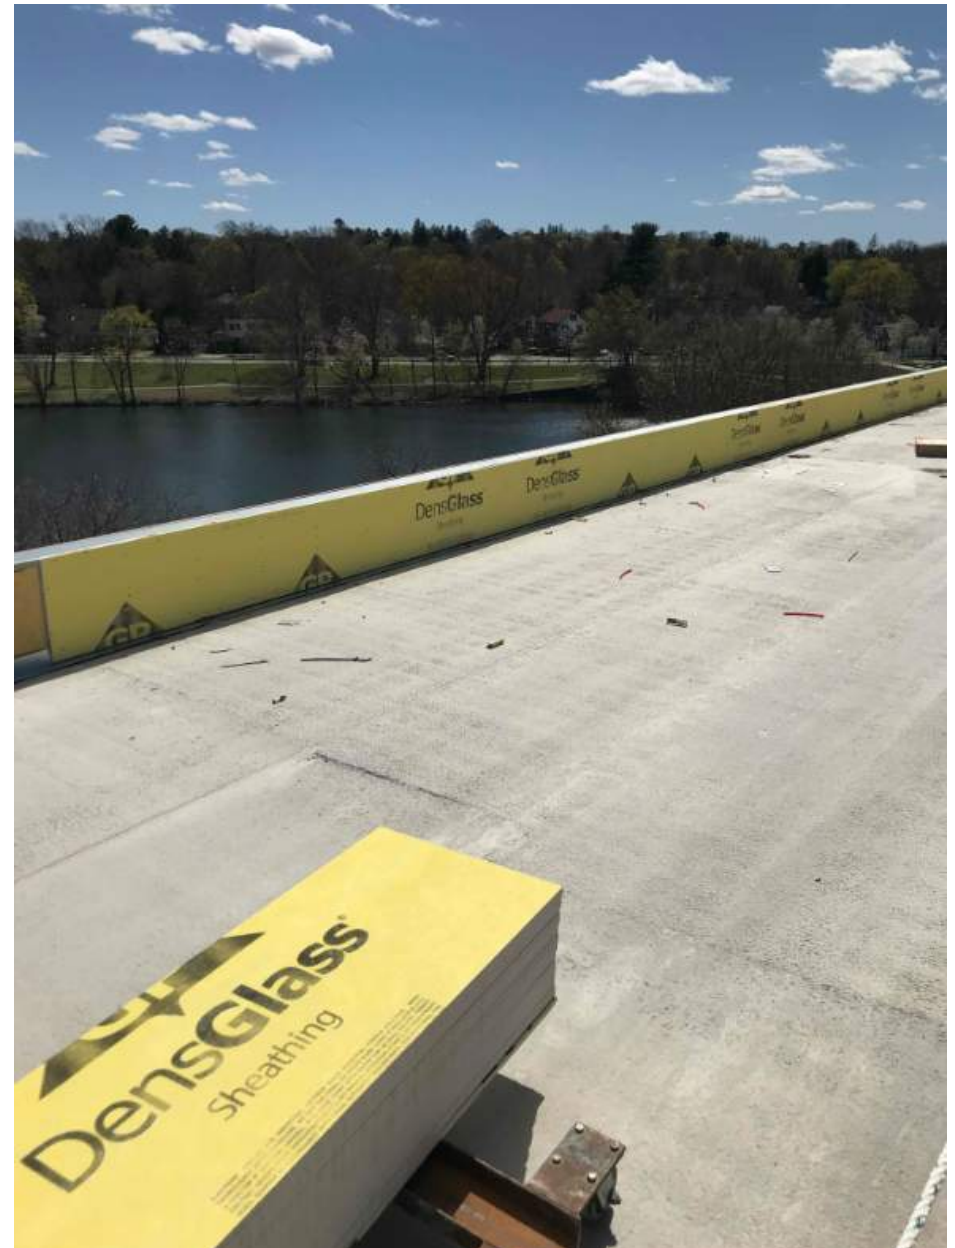

Progress Photos

- Painting of locker rooms

