

Belmont Middle & High School Project Update

June 2022

Work Performed – June 2022

Field House 9-12 Locker Room Renovation

- Continued misc. masonry restoration
- Continued installation of plumbing fixtures
- Continued installation of wall tile
- Started epoxy floor installation
- Started ACT ceiling installation
- Started installation of wall tile

Phase 2 Site Work and Utilities

- Completed reclamation of old parking lot sub grade
- Continued raising grade via existing material
- Continued installation of phase 2 utilities
 - Started preparation for porous asphalt and related utility installation

Phase 1

- Continued commissioning and balancing
- Started Summer 2022 work in Field House

Phase 2 Structure

- Continued spray fireproofing Area F slab on grade

Phase 2 Interiors

- Completed layout and top track for D wing interior partitions
- Completed layout and top track for F wing interior partitions
- Completed Elevator Core
- Completed installation of Stair 6 at D Wing
- Started installation of Stair 4
- Continued installation of overhead MEPFP's
- Continued installation of interior partition framing
- Started installation pipe and duct insulation

Phase 2 Exterior

- Continued installation of exterior framing
- Continued installation of roofing
- Continued installation of sheathing and AVB
- Continued installation of masonry at 4th floor D wing
- Continued installation of curtain-wall frames
- Started installation of curtain wall glass
- Delivered and hoisted Phase 2 Mechanical Units to roof

Look Ahead – July 2022

Field House Locker Room Renovation

- Complete installation of plumbing finishes
- Complete epoxy floor installation
- Complete installation of wall tile
- Continue misc. masonry restoration
- Start linoleum floor installation

Phase 2 Site Work and Utilities

- Continue raising grade via existing material
- Continue installation of phase 2 utilities
 - Continue preparation for porous asphalt and related utility installation
- Start electrical ductbank on Hittinger St

Phase 1

- Continue commissioning and balancing
- Continue Summer 2022 work in Field House

Phase 2 Structure

- Complete spray fireproofing F wing structure

Phase 2 Interiors

- Continue MEPFP rough-in above ceiling
- Continue installation of interior partition framing
- Continue installation pipe and duct insulation
- Start pulling electrical MC cable
- Complete Stair 4 and start Stair 5

Phase 2 Exterior

- Complete installation of exterior framing
- Complete installation of sheathing and AVB
- Complete installation of roofing
- Continue installation of curtain wall frames
- Continue installation of curtain wall glass
- Continue installation of masonry


Progress Photos

- demolition of field house bleachers




Progress Photos

- demolition of field house track

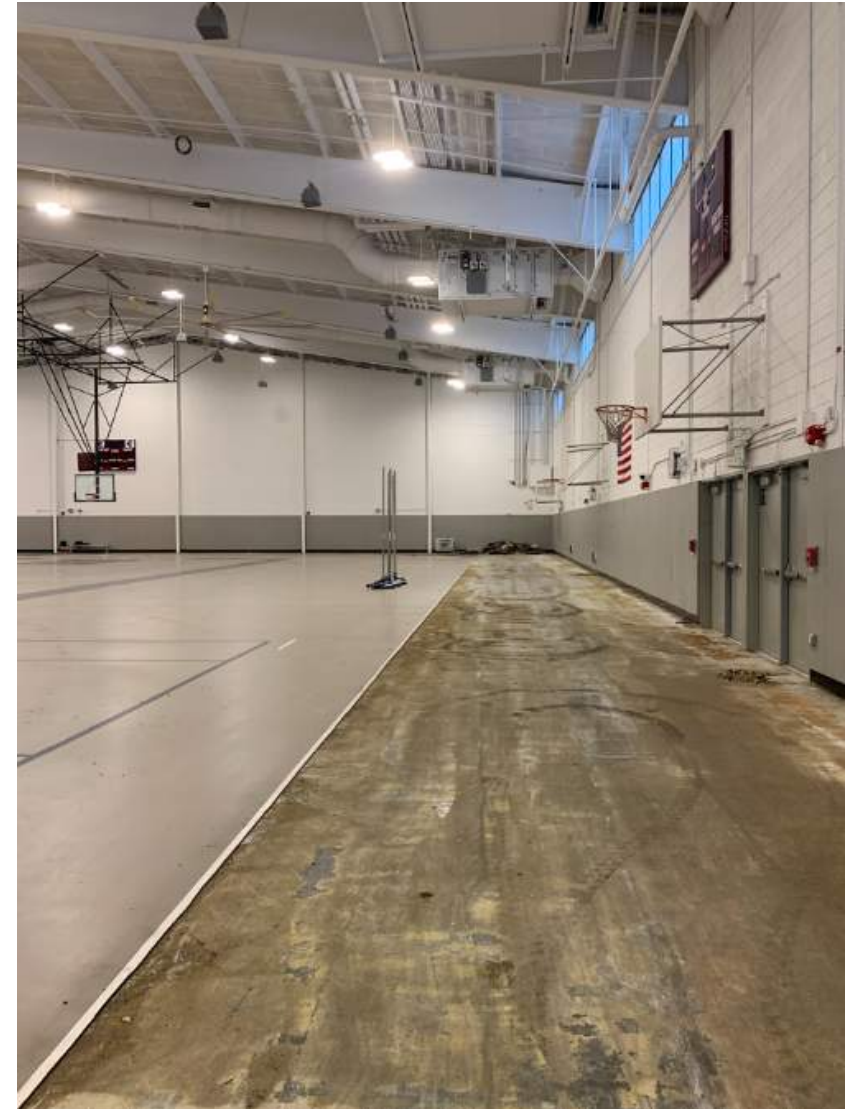

Progress Photos

- Installation of basketball hoops

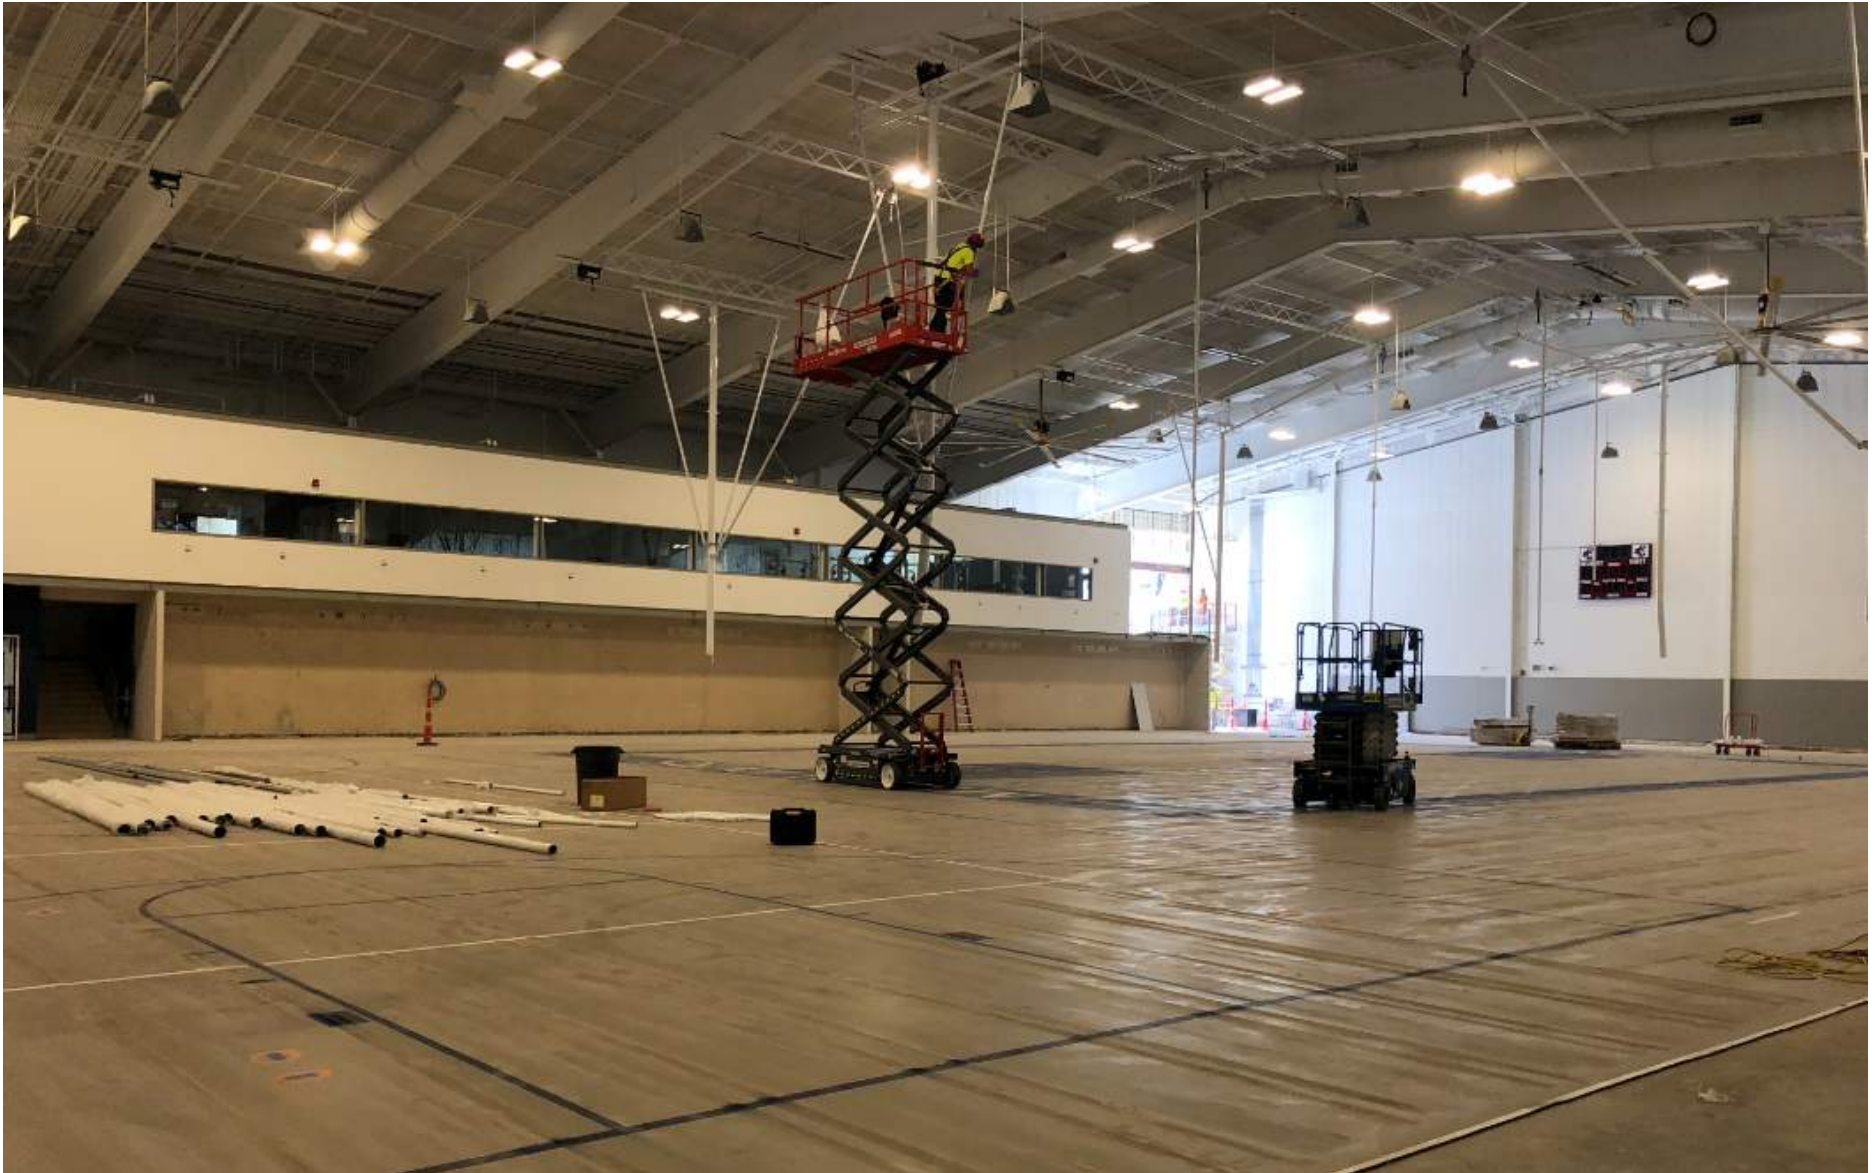

Progress Photos

- small gym renovation after temp locker room demo



- installation of wall tile in locker rooms



Progress Photos

- Continued spray fireproofing at F wing



Progress Photos

- Installation of AVB and current wall



Progress Photos

– installation of roofing and exterior sheathing




Progress Photos

- exterior framing and sheathing at mechanical well



- Completed installation of Stair 6 at D Wing

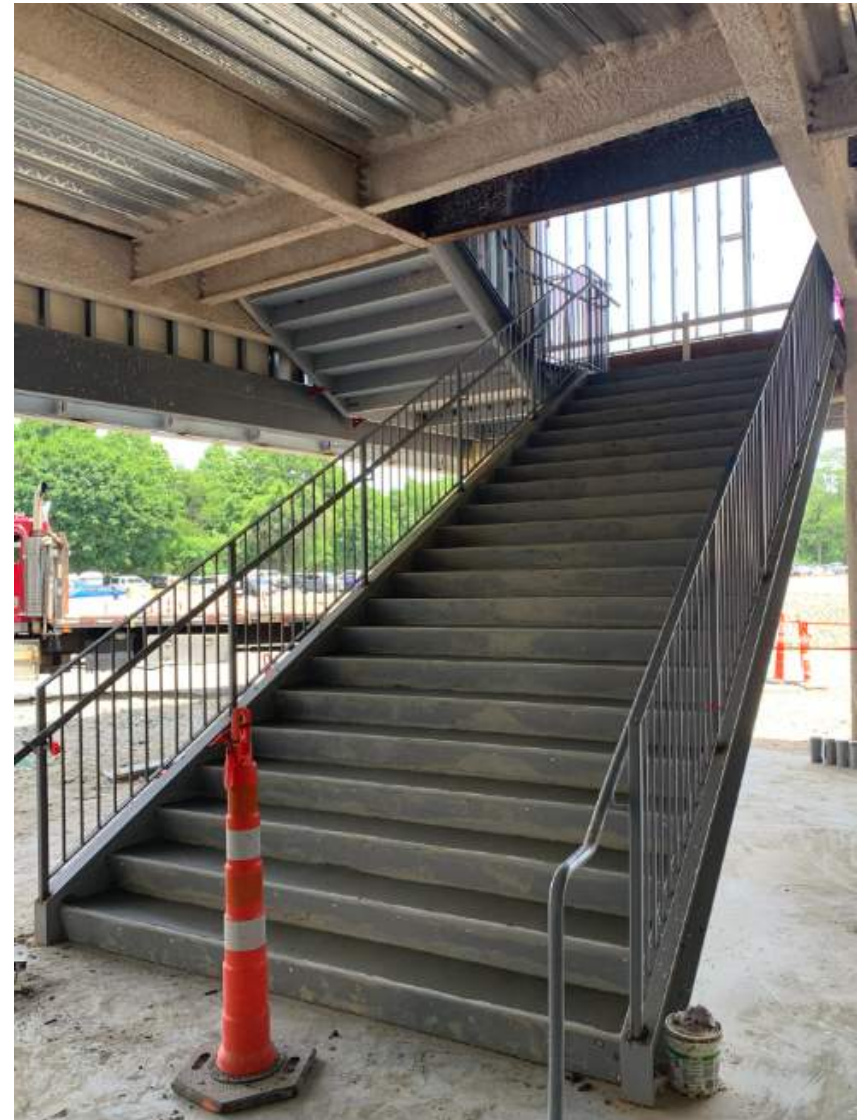

Progress Photos

- HRU's 5 & 6 in Area D Mechanical Well

