

# Belmont Middle & High School Project Update

July 2022

# Work Performed – July 2022

## Field House 9-12 Locker Room Renovation

- Completed installation of plumbing fixtures
- Completed installation of wall tile
- Completed epoxy floor installation
- Completed linoleum floor installation
- Continued misc. masonry restoration
- Continued ACT ceiling installation
- Started installation of interior doors and glazing

## Phase 1

- Continued commissioning and balancing
- Continued installation of Stair 3 wall tile
- Continued Summer 2022 work in Field House & “Splice Rooms”
  - Started installation of field house floor
  - Started re-finishing small gym floor
- Started installation of millwork at Stair 3

## Phase 2 Site Work and Utilities

- Continued raising grade via existing material
- Continued installation of phase 2 utilities
- Continued preparation for porous asphalt and related utility installation
- Started installation of athletic field drainage

## Phase 2 Structure

- Completed spray fireproofing Area F slab on grade

## Phase 2 Interiors

- Completed installation of Stair 4
- Continued rough-in of MEPFP's
- Continued installation of interior partition framing
- Continued installation pipe and duct insulation
- Started installation and finishing of drywall – Area D Level 2
- Started pulling electrical feeder wire from Phase 1 to Phase 2
- Started installation of hollow metal frames
- Started installation of Stair 5

## Phase 2 Exterior

- Completed installation of exterior framing
- Completed installation of roofing
- Completed installation of sheathing and AVB
- Continued installation of masonry on D wing façade
- Continued installation of curtain-wall frames
- Continued installation of curtain wall glass
- Started installation of masonry on F wing façade

# Look Ahead – August 2022

## **Field House Locker Room Renovation**

- Complete misc. masonry restoration
- Complete ACT ceiling installation
- Complete installation of interior doors and glazing

## **Phase 1**

- Continue commissioning and balancing
- Complete installation of Stair 3 wall tile
- Complete installation of millwork at Stair 3
- Complete Summer 2022 work in Field House & “Splice Rooms”
  - Complete installation of Field House floor
  - Complete re-finishing of Small Gym floor

## **Phase 2 Site Work and Utilities**

- Continue raising grade via existing material
- Continue installation of athletic field drainage
- Continue installation of phase 2 utilities
- Complete installation of porous asphalt

## **Phase 2 Interiors**

- Complete installation of interior partition framing
- Complete pulling electrical feeder wire from Phase 1 to Phase 2
- Continue rough-in of MEPFP’s
- Continue installation pipe and duct insulation
- Continue installation and finishing of drywall
- Continue installation of hollow metal frames

## **Phase 2 Exterior**

- Continue installation of curtain wall frames
- Continue installation of curtain wall glass
- Continue installation of masonry

# Progress Photos

– Field House Floor



# Progress Photos


- Re-finishing of Small Gym floor





# Progress Photos

- Auditorium balcony and orchestra pit railings

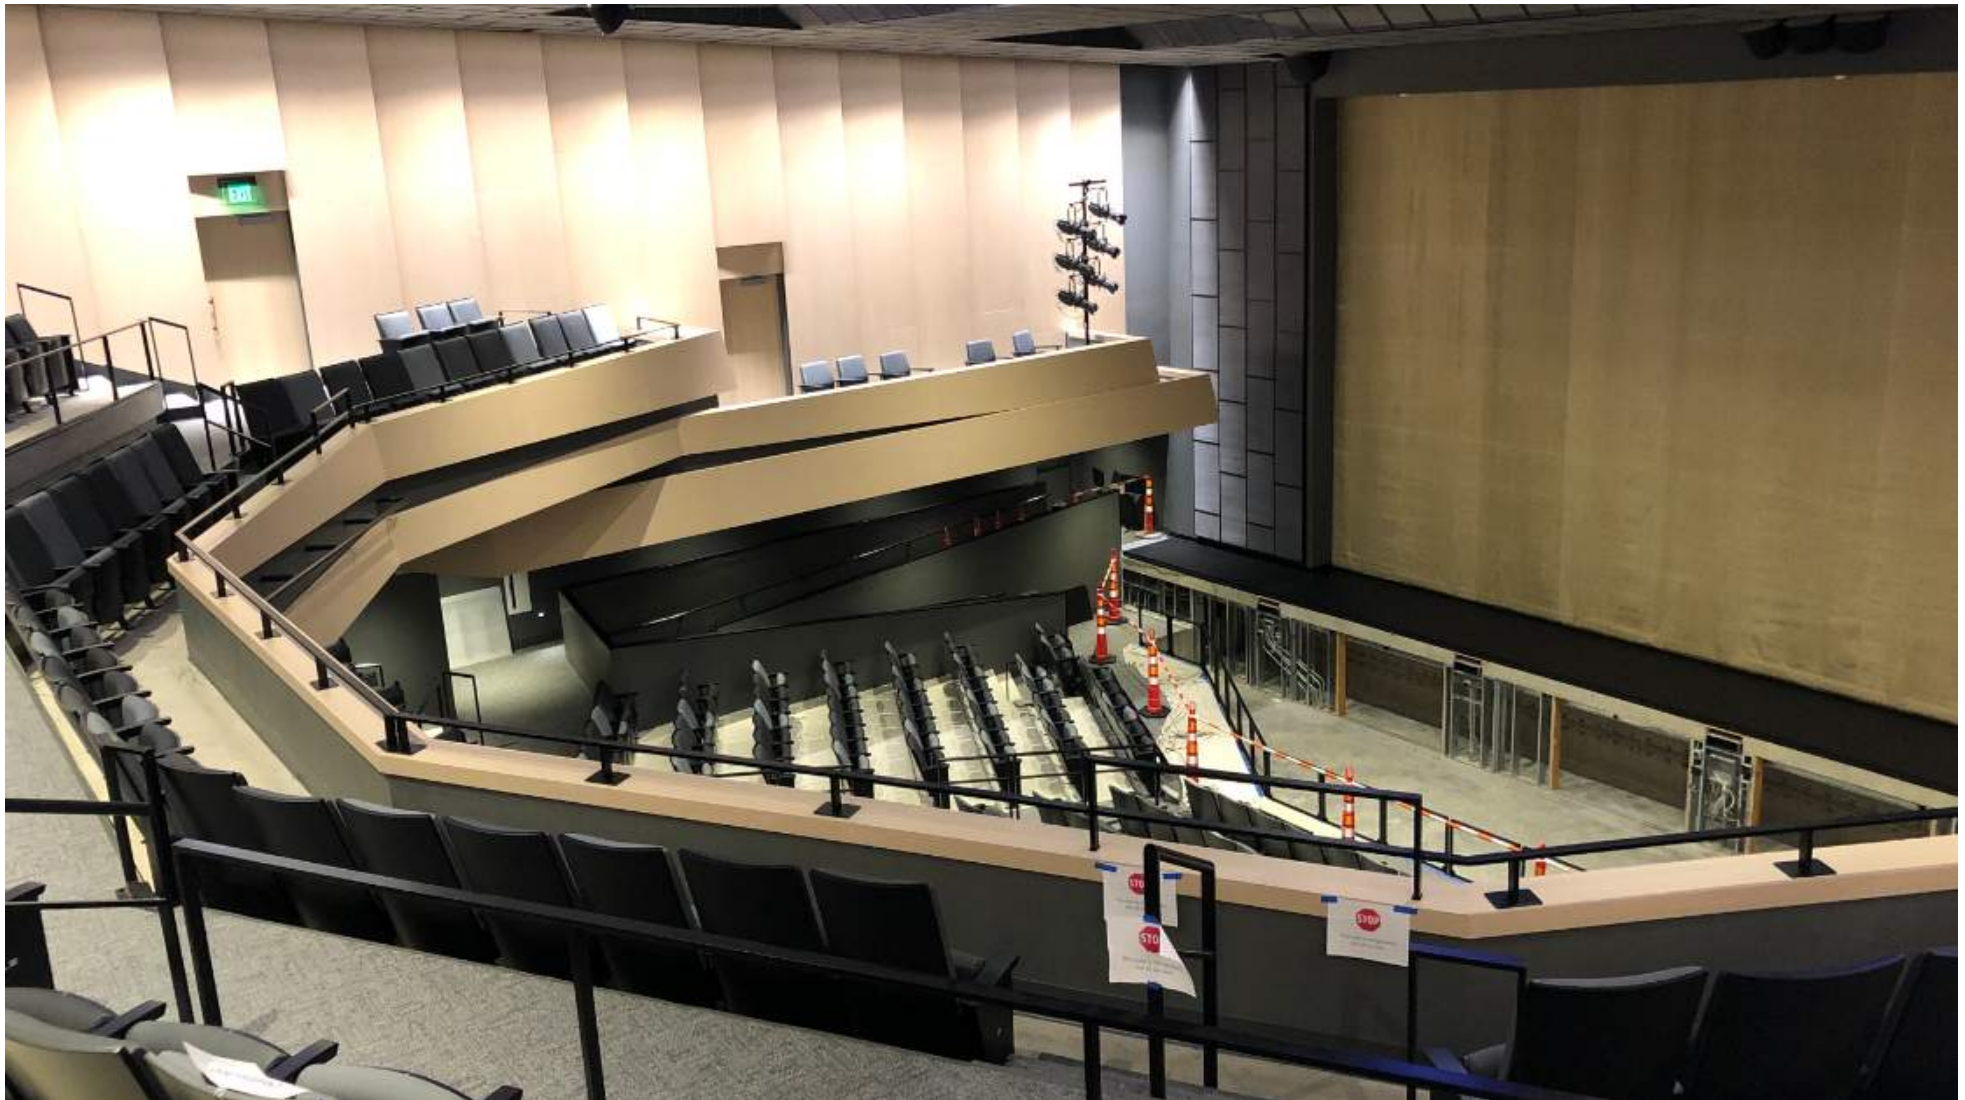

# Progress Photos

– Stair 3 Millwork



# Progress Photos

- Locker Room Bathroom Finishes





# Progress Photos

- Framing and Drywall at D Wing, Level 2



# Progress Photos

- Drywall in typical classroom






# Progress Photos

- Topping slab over radiant floor in Area D, Level 1



- Stair 4 rough installation

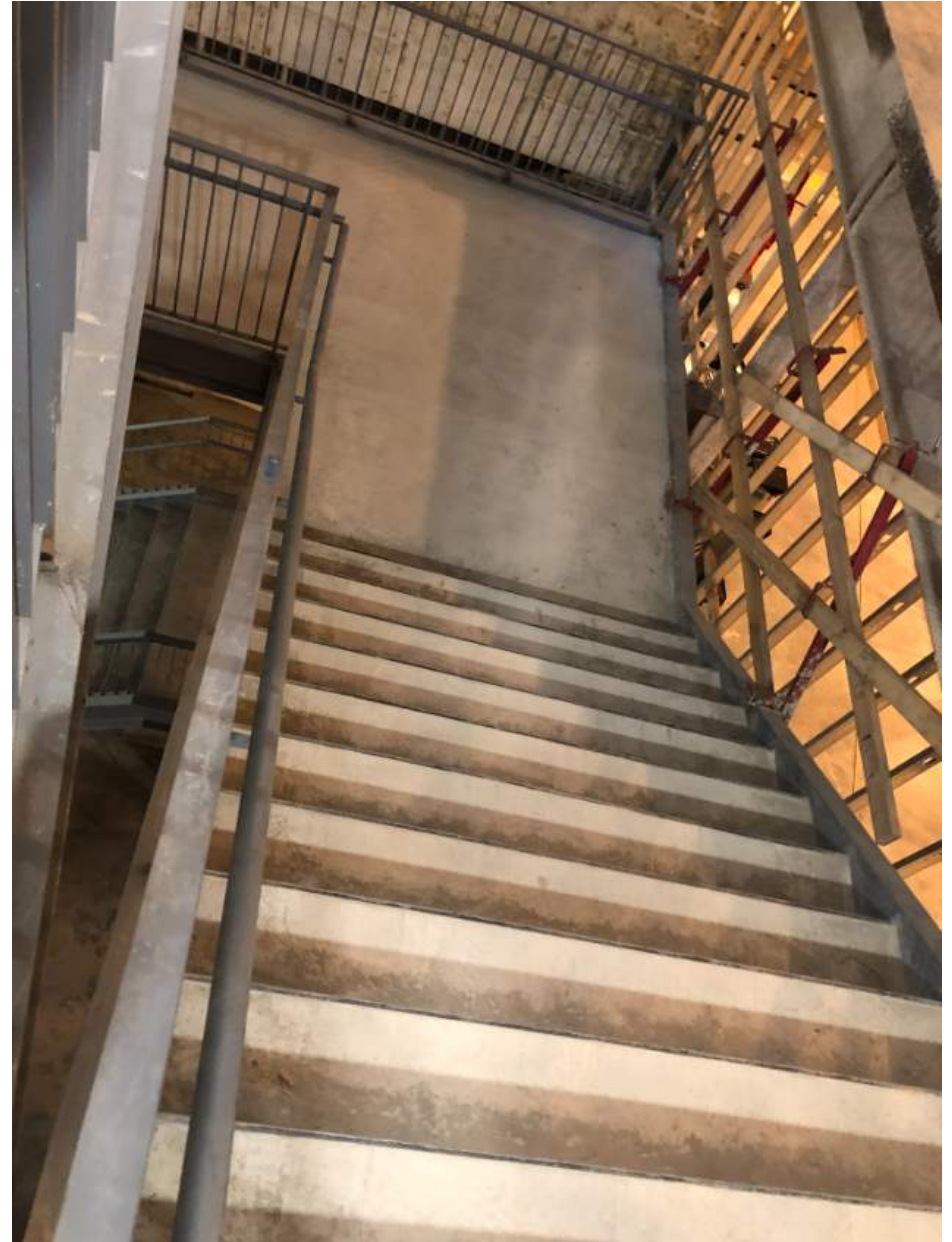



# Progress Photos

- Preparation for porous asphalt



- Masonry installation at Area D

