

Belmont Middle & High School Project Update

June 2021



Work Performed – May 2021

General

- Continued Incorporating COVID-19 Provisions on Site for Safe Work Practices
- Continued start-up of HVAC systems
- Removed scaffold staging in Pool and Auditorium
- Continued installation of roadway and curbs
- Completed moving Skanska and CHA trailers to Phase 2 location

Building A

- Completed installation of classroom and corridor flooring
- Completed installation of bathroom tile
- Completed installation of epoxy floor in bathrooms
- Completed installation of classroom lighting
- Completed installation of classroom doors
- Continued installation of multi-story curtain wall at HS Main Entrance Canopy
- Continued installation of electrical outlets and devices
- Continued installation of casework in classrooms
- Started installation of carpet flooring
- Started installation of bathroom finishes
- Started installation of acoustic ceiling tiles
- Started installation of window shades

Building B

- Completed above ceiling punch list
- Completed installation of glass and metal panels at windows

Building B continued

- Completed installation of classroom lighting
- Completed installation of ceiling grid
- Completed installation of epoxy floor in bathrooms
- Continued installation of classroom and corridor flooring
- Continued installation of High School elevator
- Started installation of classroom doors
- Started installation of bathroom finishes
- Started installation of acoustic ceiling tiles
- Started installation of electrical outlets and devices
- Started installation of tiered seating structure in Auditorium

Building C

- Completed installation of baffle ceiling at pool
- Completed installation of Stair 14 in Area C Mechanical Well
- Continued installation of drywall and wall finishes
- Continued painting primer and first finish coat on interior walls
- Continued installation of ACT ceiling grid
- Continued installation of kitchen equipment and finishes
- Continued installation of glass and metal panels at windows
- Continued above ceiling punch list
- Started installation of classroom and corridor flooring
- Started installation of corridor tile
- Started installation of Armstrong acoustic drywall ceiling (ACT-14)

Look Ahead – June 2021

General

- Continue start-up of HVAC systems
- Complete installation of roadway and curbs
- Start Summer 21' Field House renovation
- Start installation of roll-up and accordion fire doors

Building A

- Complete installation of interior office doors
- Complete installation of Level 1 carpet
- Complete installation of casework
- Complete installation of multi-story curtain wall glass at Main HS Entrance
- Complete installation of bathroom finishes
- Complete installation of window shades
- Start installation of exterior doors
- Start final Punch List

Building B

- Complete application of final paint
- Complete installation of corridor and classroom flooring
- Complete installation of light fixtures and other ceiling devices
- Complete installation of acoustic ceiling tiles
- Continue installation of tiered seating structure

Building B continued

- Start classroom casework installation
- Start installation of large format floor tile
- Start installation of exterior doors
- Start installation of window shades
- Start final Punch List

Building C

- Complete installation of Stair 3
- Complete above ceiling punch list
- Complete installation of glass and metal panels at windows
- Complete installation of roofing of low roofs and mechanical well
- Continue installation of light fixtures and other ceiling devices
- Continue installation of kitchen equipment
- Continue installation of Armstrong acoustic drywall ceiling (ACT-14)
- Continue installation of corridor tile
- Continue installation of classroom flooring
- Start installation of large format floor tile
- Start application of final paint

Progress Photos

- Installation of Armstrong acoustic drywall ceiling (ACT-14)



- Installation of roadway and curbs



Progress Photos

- Installation of tiered seating structure in Auditorium



- Servery Tile



Progress Photos

- Installation of casework and electrical devices



Progress Photos

Installation of Millwork Wall (left) and Ceilings at Stair 3 (middle)



Progress Photos

- Installation of bathroom partitions



- Installation of carpet




Progress Photos

- Installation of interior glass



- Installation of classrooms lighting

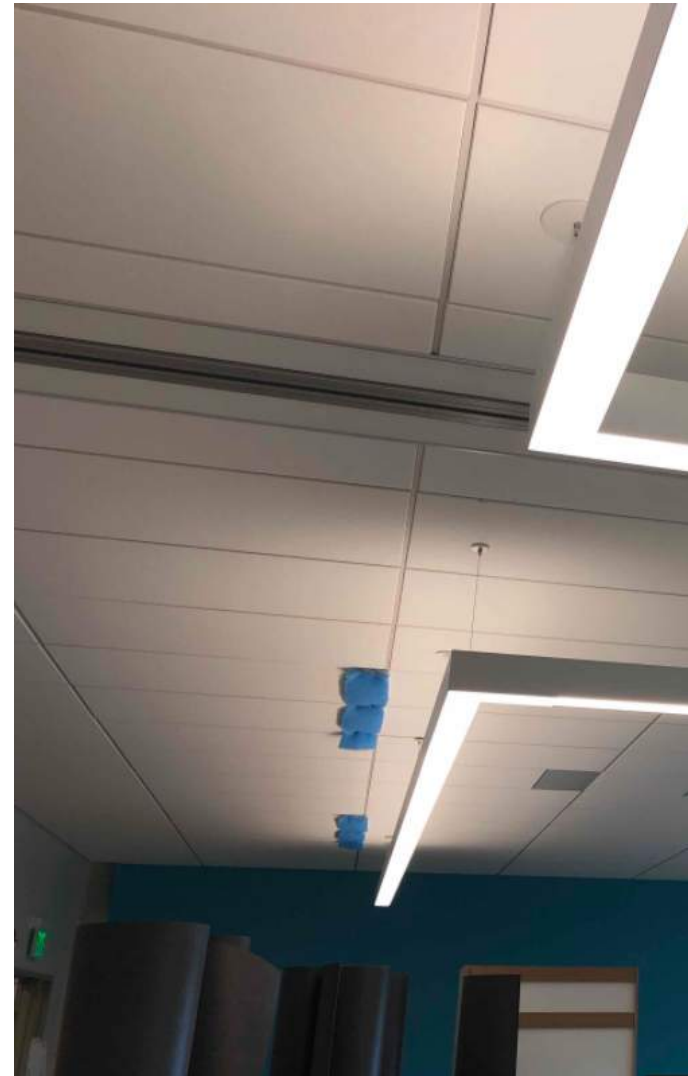


Progress Photos

- HS Main Entrance



Progress Photos

- Auditorium Ceiling

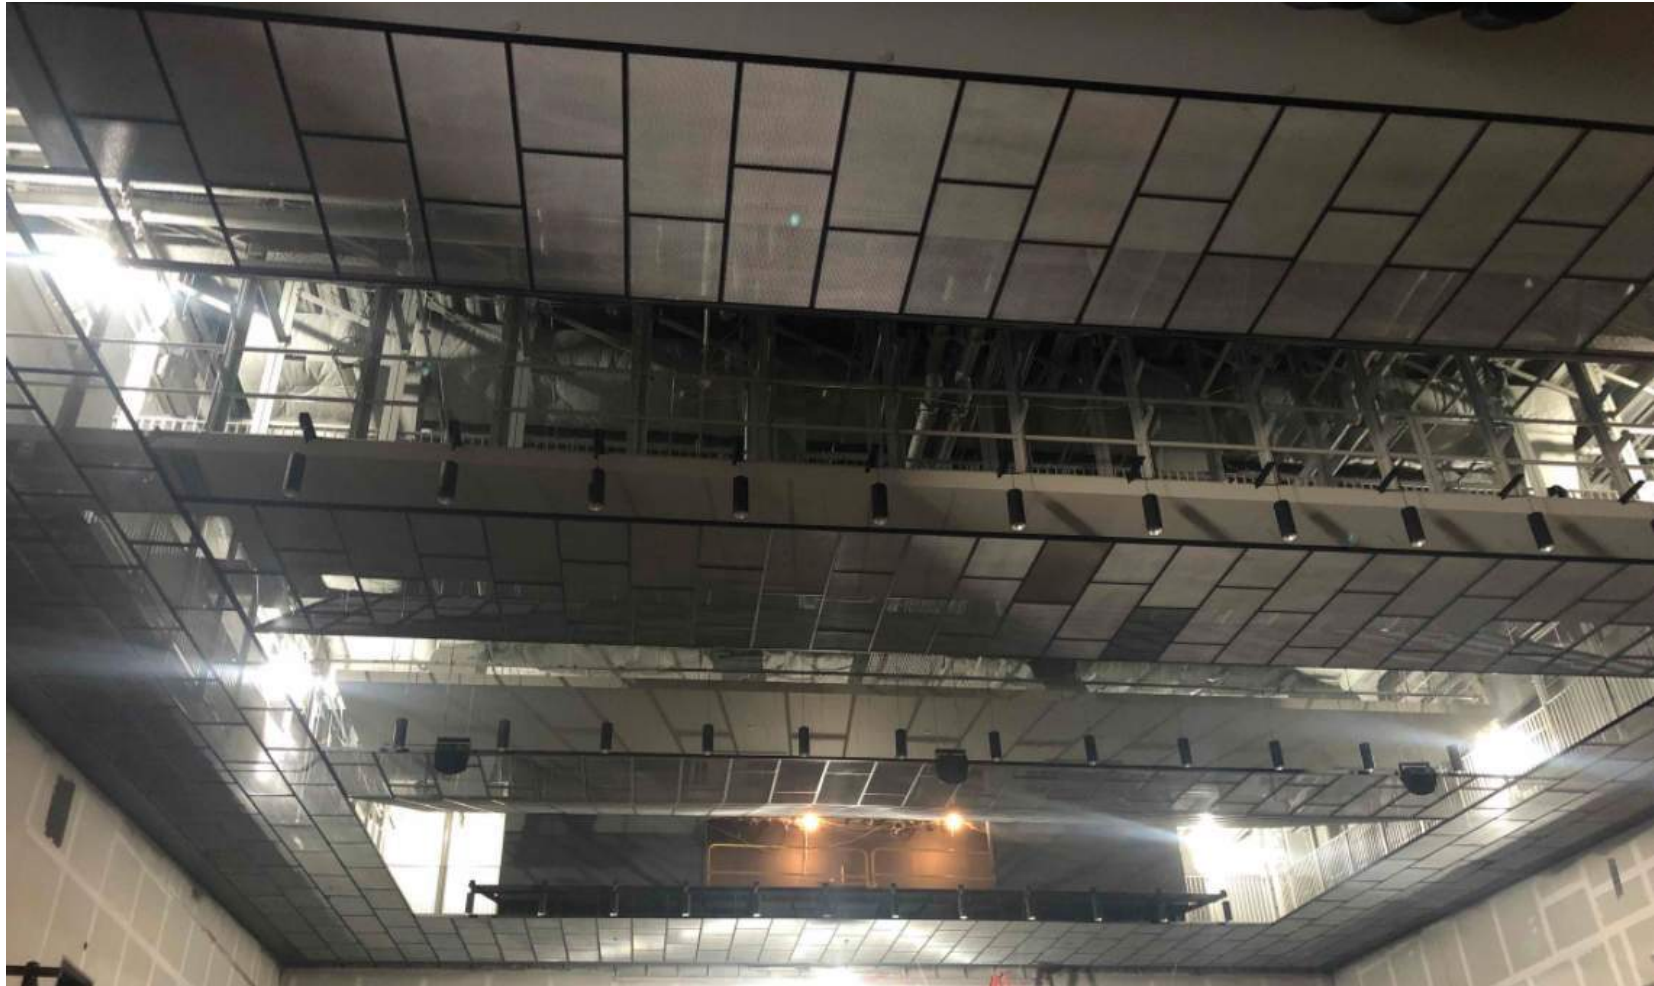

Progress Photos

- Typical classroom finishes

