

Belmont Middle & High School Project Update

August 2021



Work Performed – August 2021

General

- Received TCO for Phase 1
- Continued start-up, testing and balancing of HVAC systems
- Continue Punch List effort
- Continued asbestos abatement in old school
- Started demolition of old school

INSPECTIONS

- Board of Health
- Final Plumbing
- Final Electrical
- Final Building and HVAC
- Final Building Commissioner
- Final Fire Department

Exterior

- Completed rework of site fence to facilitate Phase 2 work
- Completed Sidewalk and Hardscape Prep
- Completed Phase 1 traffic improvements and striping
- Completed Site Prep for Landscaping
- Continued work at Turf Field
- Start hydroseed and lawn development

Building A

- Completed installation of multi-story curtain wall at HS Main Entrance Canopy
- Completed A2 – A4 Corridor Final Finishes
- Continued FFE for A1-A4

Building B

- Continued Final Cleaning and Punch List B4 – B2
- Continued FFE B4 – B2
- Continued work in Auditorium
- Completed Atrium Railing System

Building C

- Completed Painting and Wall Finishes – C1 – C4
- Completed ACT 6, 12, 14 Installation
- Completed installation of classroom and corridor flooring
- Completed installation of corridor tile
- Completed ACT-14 Installation C4, C3, C2 and C1 (Kitchen)
- Completed Kitchen/Servery Finish Installation
- Continued with Pool Finishes
- Continued punch list and final cleaning

Field House

- Completed Summer 2021 work
- Started final cleaning

Look Ahead – September 2021

General

- Complete start-up, testing and balancing of HVAC systems
- Continue commissioning MEP systems
- Continue Punch List effort

Exterior

- Continue Turf Field Installation
- Continue lawn development

Building B

- Continued work in Auditorium and Black Box

Building C

- Complete Start-Up of Kitchen and Servery
- Continue with Pool Finishes

Field House

- Continue 1st floor locker room renovation

Phase 2

- Complete asbestos abatement in old school
- Continue demolition of old school
- Continue Phase 2 site utilities
- Start site preparations for pile driving

Progress Photos

- High School Main Entrance / Drop off Loop



Progress Photos

– High School Main Entrance / Drop off Loop



Progress Photos

- Areas A and C South Elevation



Progress Photos

- Areas A and B



- Corridor B100



Progress Photos

- Corridor A100A



- Corridor B100



Progress Photos

- Café Commons



Progress Photos

- Corridor A200




- Corridor C200



Progress Photos

- Field House Renovation

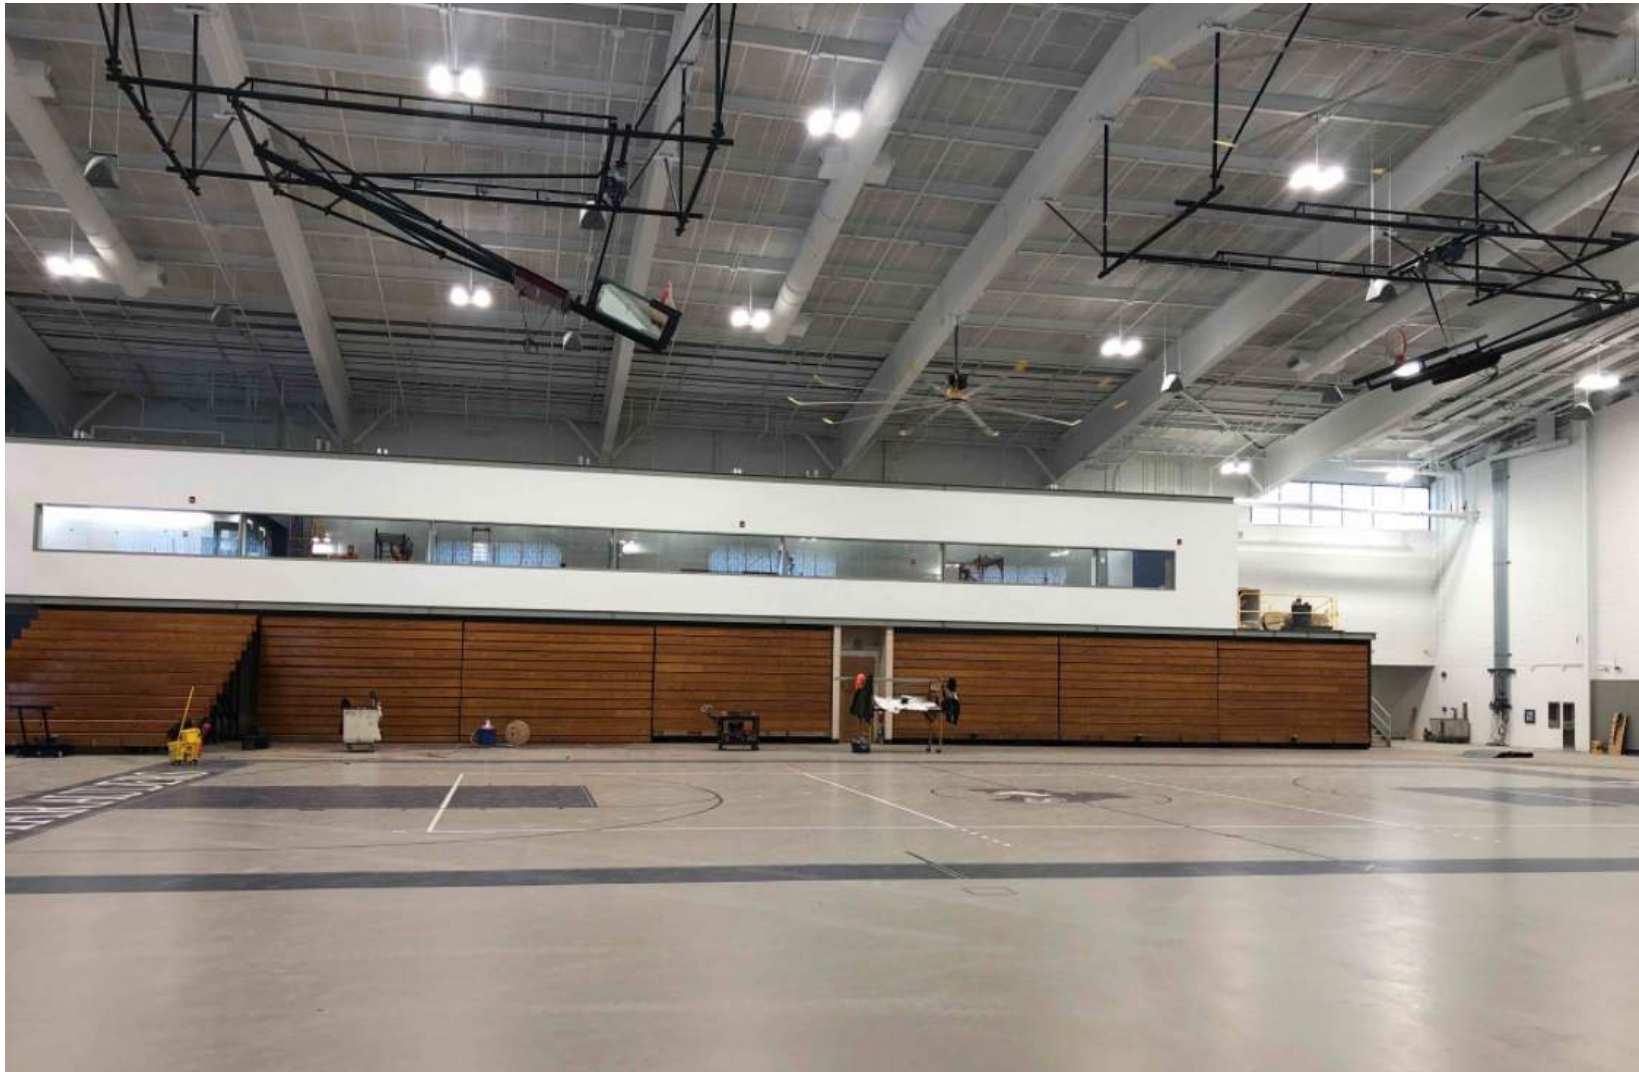


Progress Photos

- Demolition of old High School



Progress Photos

- Demolition of old High School boiler room

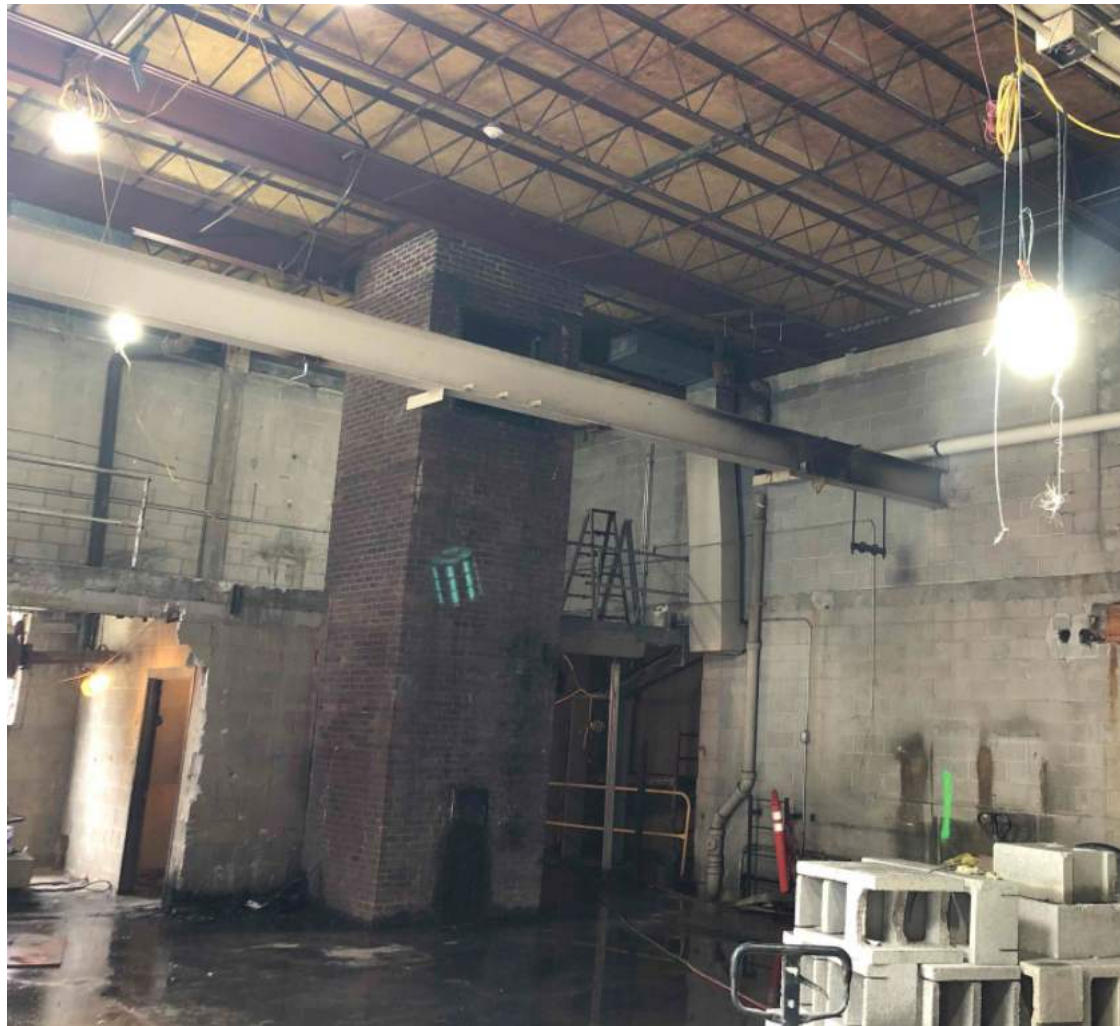

Progress Photos

- Old High School during abatement



Progress Photos

- Demolition of old High School

