


SKANSKA

Belmont Middle & High School Project Update

May 2023



Work Performed – May 2023

Phase 1:

- Preparation for Summer Work
- Ceilings in Locker Rooms
- MS & Team Room Lockers

Phase 2 Site Work and Utilities:

- Started moving PV panels to roof
- Baseball Bleachers
- Hydroseeding/Field Development

Phase 2 Interiors:

- Painted Stairs
- Hallway Tackboard Installation

Area D:

- **Punchlist**
- **Commissioning**
- **Furniture Delivery**

Area F:

- **Punchlist**
- **Commissioning**
- **Furniture Delivery**

Look Ahead – June 2023

Phase 2 Site Work and Utilities:

- Raising Site Utility Structures
- Baseball/Softball Field Development
- Sod installation
- Temp Parking Lot Removal

Phase 2:

- Punchlist
- Commissioning

Summer Phasing Work

- Set up Protection in corridors
- Demolish Temp Wellness Rooms
- Demolish Stair 4
- Casework Install in Temp IT Suite

PV Scope

- Pull Feeders to electric Room from PH 2 Closets
- Install Disconnect Switches by Loading Dock
- Wire Emergency Shut Offs
- Deliver Materials/Hoist to Roof

Progress Photos

Exterior



Progress Photos

Exterior



Progress Photos

Sod



Progress Photos

Sod



Progress Photos

Softball bleachers



Progress Photos

Media center



Progress Photos

Classroom



Progress Photos

Science room




Progress Photos

Science prep room



Progress Photos

Restrooms

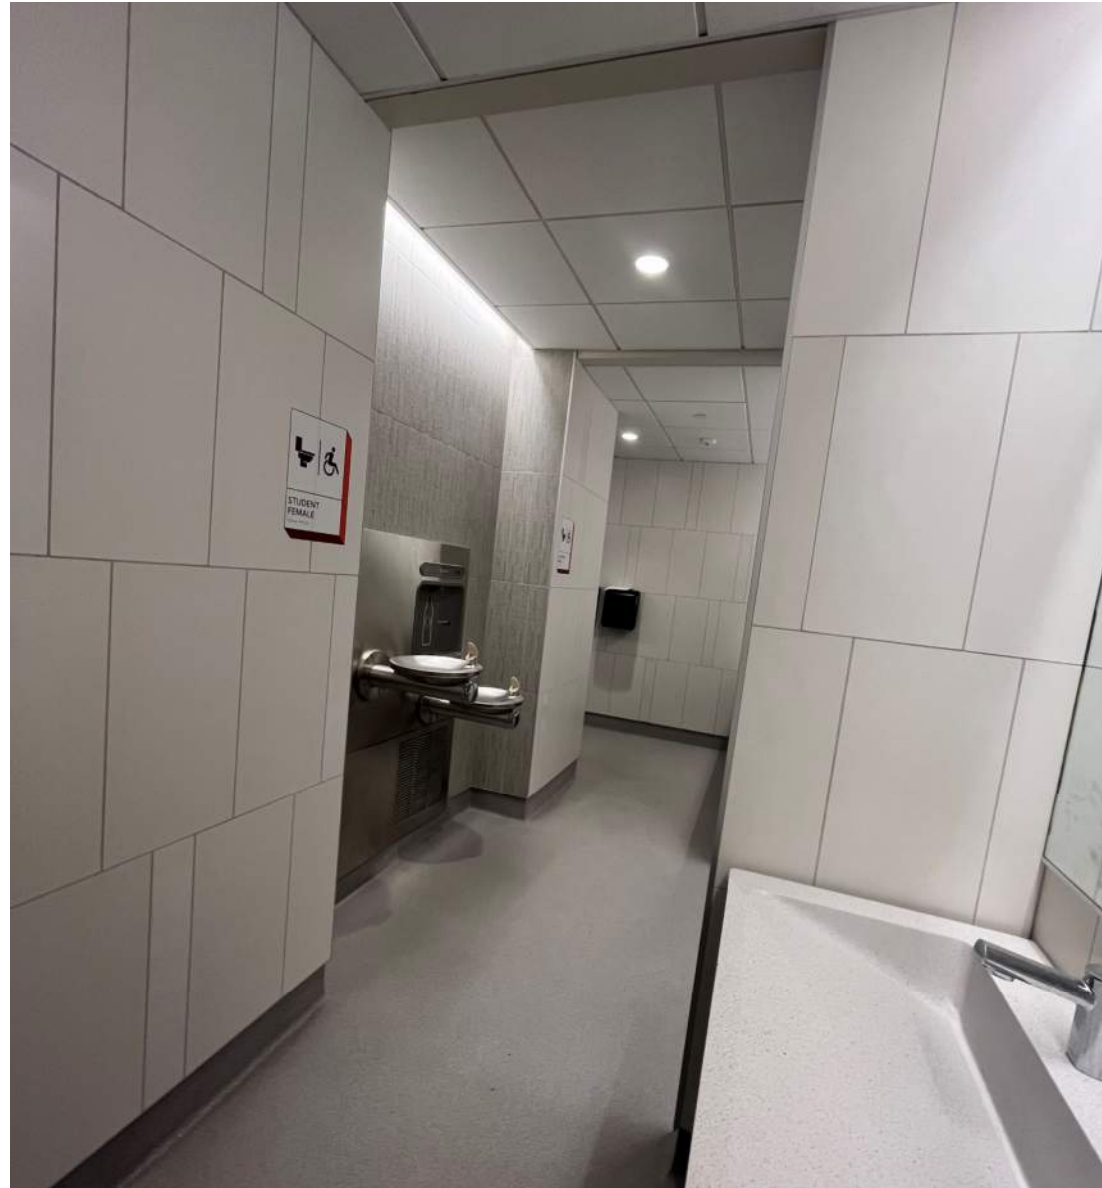

Progress Photos

Directors room



Progress Photos

Middle School Stair



Progress Photos

Protection



Progress Photos

PV panels on roof



Progress Photos

PV panels on roof



Progress Photos

PV panels on roof

