

Belmont Middle & High School Project Update

May 2020

April 2020 Work Performed

- Completed Geothermal Well-Field #1 Drilling and Started Lateral Piping.
- Continued Drilling in Geothermal Well-Field #2.
- Placed Level 3 Building B and Level 2 Building A.
- Continued Installing Radiant Tubing within Concrete Slabs on Metal Deck.
- Continued Erecting/Decking and Detailing Building C/D Structural Steel.
- Completed Erecting Building A & Building B Structural Steel.
- Started Under-slab Utility Installation in Building A.
- Started Interior/Exterior Wall Layout and Top Track Installation Prior to Fireproofing.
- Continued MEP/FP Coordination.
- Continued Incorporating COVID-19 Provisions on Site for Safe Work Practices.



Photo 1 – Commencement of Lateral Geothermal Piping Installation.



Photo 2 – Geothermal Well Drilling in Field #2..



Photo 3 – Finishing Level 3 Building B Slab.



Photo 4 – Finishing Level 2 Building A Slab.



Photo 5 – Radiant Tubing Installed Within Slab on Metal Deck.



Photo 6 – Erecting Steel in Building C/D.



Photo 7 – Building A and B Erection Completed.



Photo 8 – Under-slab Utility Work in Building A.

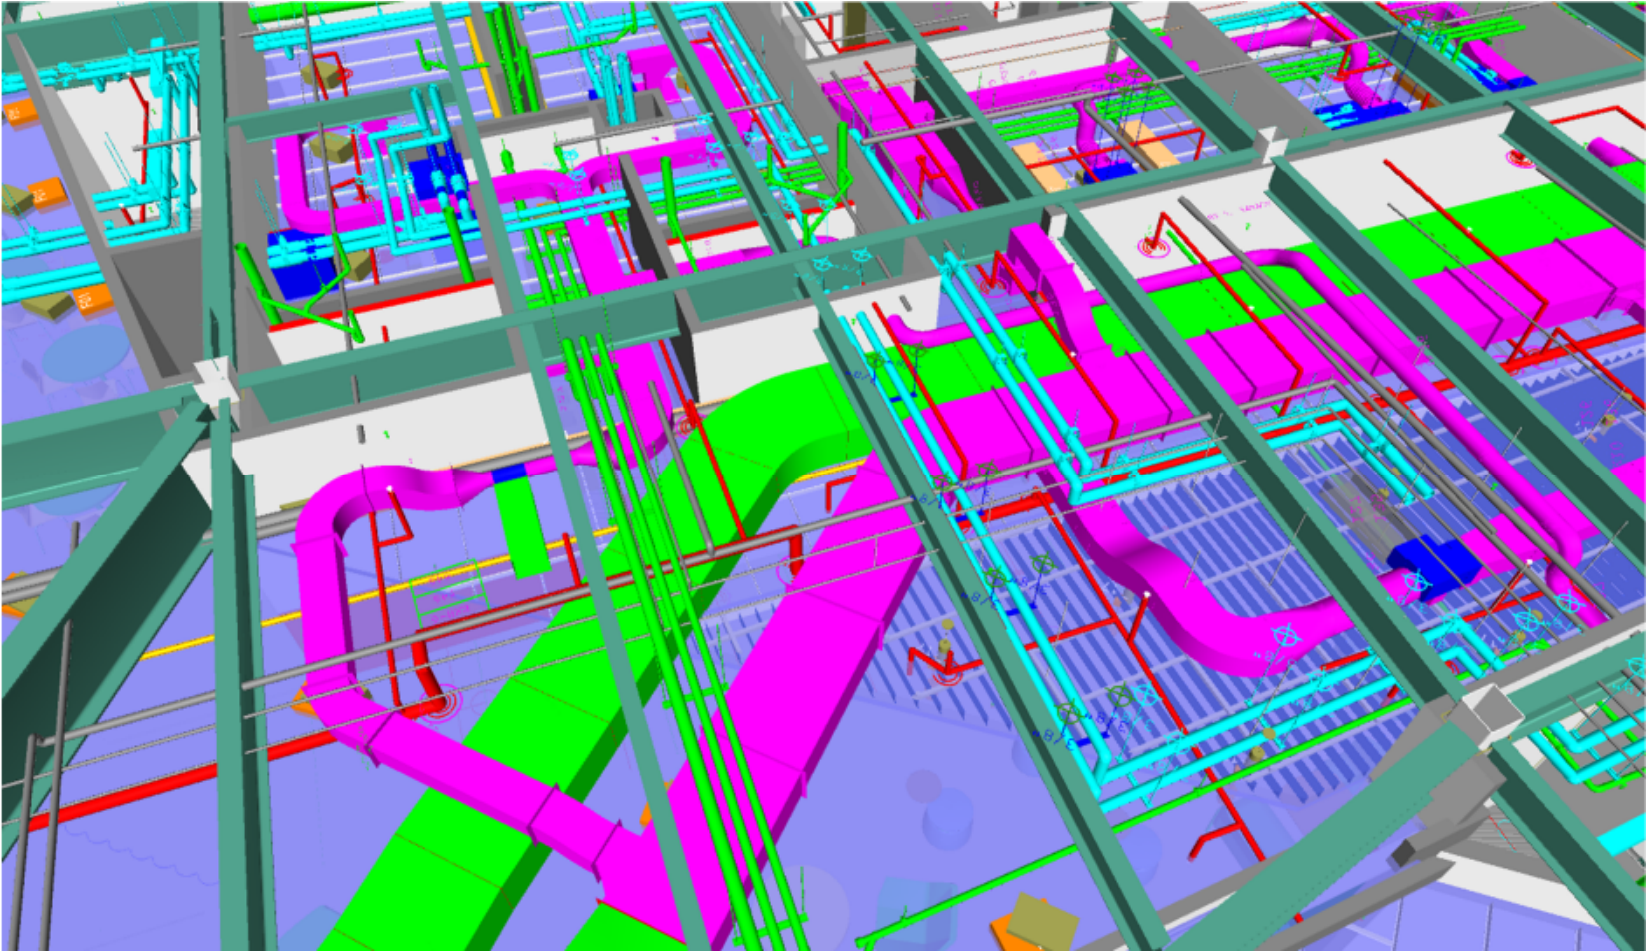


Photo 9 – MEP/FP Coordination Model
Snap Shot.



Photo 10 – COVID-19 Face Covering PPE Signage.



Photo 11 – Workers with Face Covering PPE.



Photo 12 – Hand Wash Station Map Signage.



Photo 13 – Trades Using Permanent Hand Wash Stations.

May 2020 Look-Ahead

- Complete Drilling Geothermal Wells in Field #2 and Continue Lateral Piping.
- Continue Radiant Tubing Installation on Building A, B & C.
- Complete Structural Steel Erection and Celebrate Topping-Out.
- Continue Decking and Detailing in Building C.
- Continue Concrete Slab on Metal Deck Placements.
- Continue Interior Wall Layout and Top Track Installation.
- Continue MEP/FP Coordination.
- Start Spray Fireproofing of Structural Steel.
- Start Exterior Wall Framing.
- Continue Under-slab Utility Installation Building A, B & C.
