

Belmont Middle & High School Project Update

July 2021



Work Performed – July 2021

General

- Continued start-up, testing and balancing of HVAC systems
- Continue Punch List effort

Exterior

- Completed Phase 1 Roadway Remediation
- Continued Sidewalk and Hardscape Prep
- Continued Site Prep for Landscaping
- Started work at Turf Field

Building A

- Continued installation of multi-story curtain wall at HS Main Entrance Canopy
- FFE Floor A1
- FFE Floor A2
- FFE Floor A3
- FFE Floor A4
- Continued A2 – A4 Corridor Final Finishes

Building B

- Completed Floor B4
- Completed Floor B3
- Started Final Cleaning and Punch List B4 – B2
- FFE Started B4 – B2
- Continued work in Auditorium
- Continued Atrium Railing System
- Completed B1 Large Format Floor Tile

Building C

- Continued Painting and Wall Finishes – C1 – C4
- Continued ACT 6, 12, 14 Installation
- Continued above ceiling punch list and Sign-off
- Continued installation of classroom and corridor flooring
- Continued installation of corridor tile
- Continued ACT-14 Installation C4, C3, C2 and C1 (Kitchen)
- Continued Kitchen/Servery Finish Installation
- Continued with Pool Finishes

Field House

- **Continued Field House Renovation**

Look Ahead – August 2021

General

- Continue start-up, testing and balancing of HVAC systems
- Continue Punch List effort

Exterior

- Complete all Phase 1 Roadway Work
- Complete all Phase 1 Sidewalk and Hardscape Prep
- Continued all Phase 1 Landscaping
- Continue Turf Field Installation

Building A

- Complete Main Entry Canopy
- FFE Floor A1
- FFE Floor A2
- FFE Floor A3
- FFE Floor A4

Building B

- FFE Floor B4
- FFE Floor B3
- FFE Floor B2
- Complete Construction B1
- FFE B1
- Continued work in Auditorium

Building C

- Complete Floor C2
- Complete Floor C3
- Complete Floor C4
- Complete Floor C1
- FFE Floors C1 – C4
- Continue Start-Up of Kitchen and Servery
- Continue with Pool Finishes

Field House

- Complete Field House Renovation

INSPECTIONS


- **Board of Health**
- **Final Plumbing**
- **Final Electrical**
- **Final Building and HVAC**
- **Final Building Commissioner**
- **Final Fire Department**

Progress Photos

- ACT-14 ceiling at Stair 3




- Installation of lockers

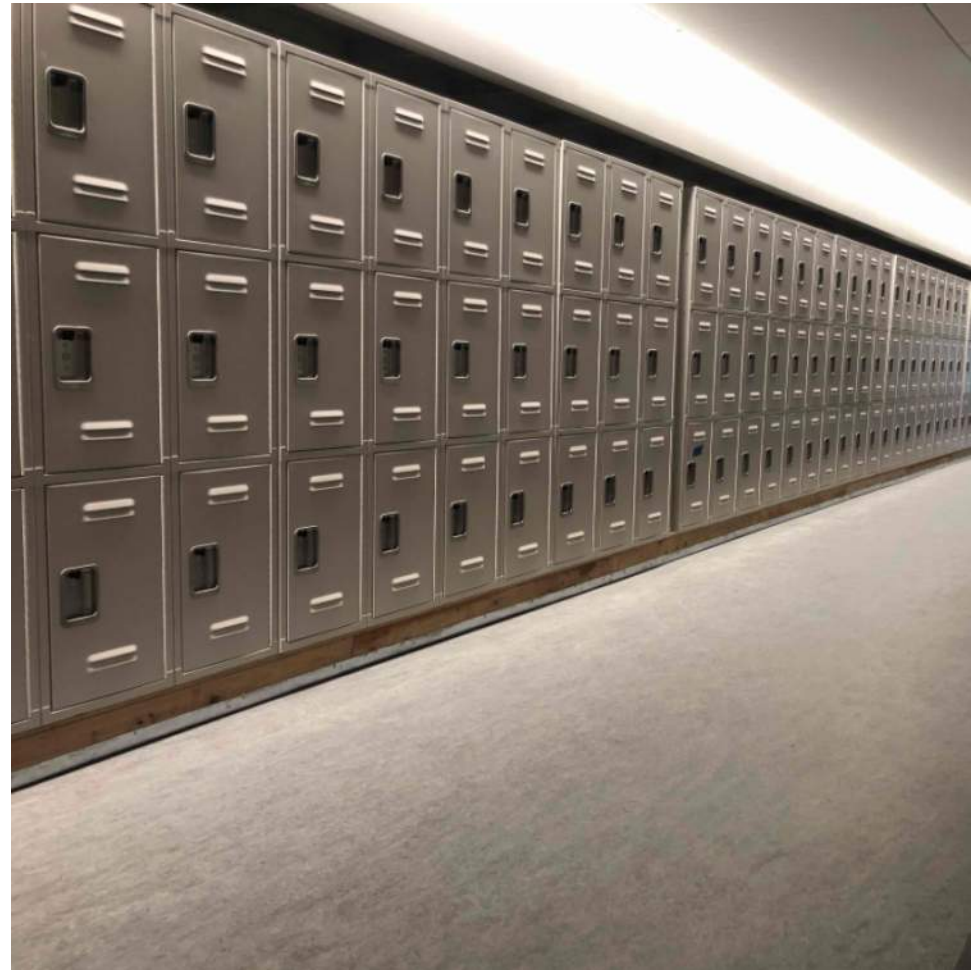


Progress Photos

- Installation of drainage around Rugby Field

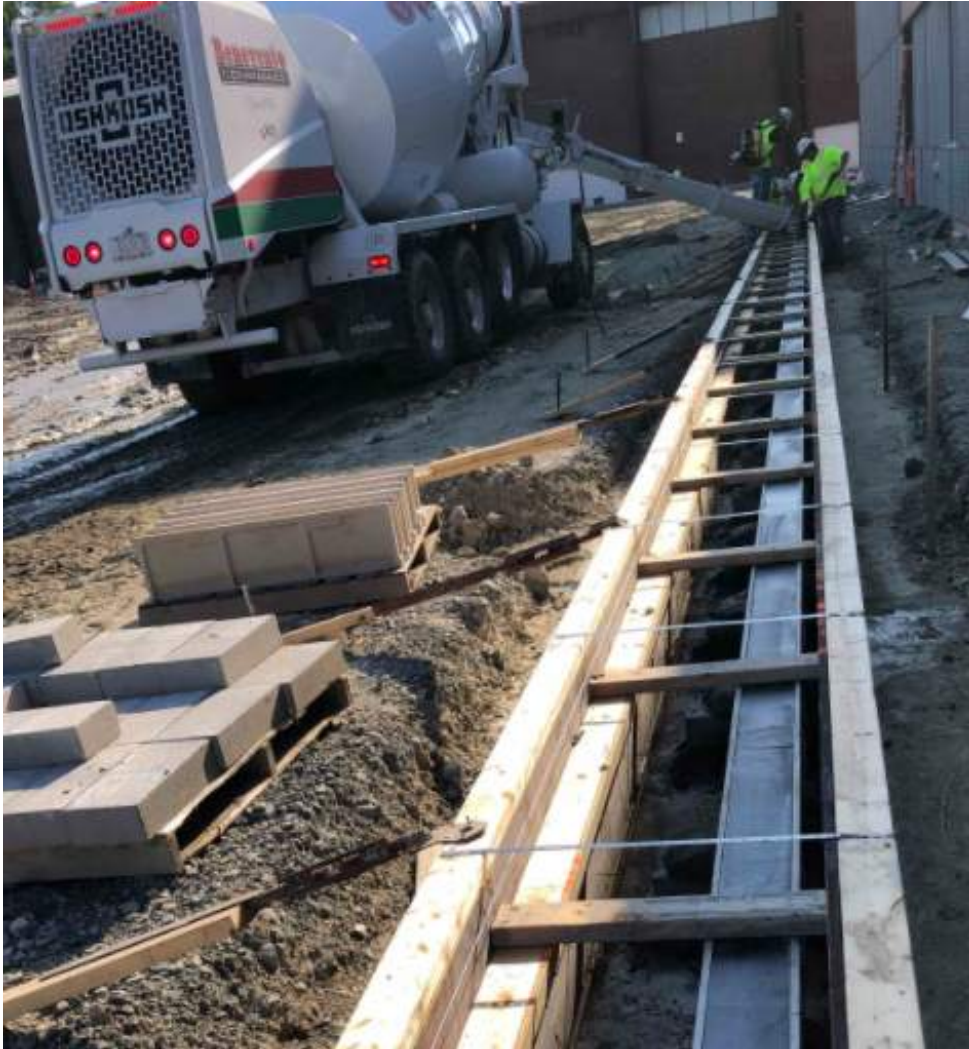


Progress Photos

- Installation Mezzanine structure in Field House

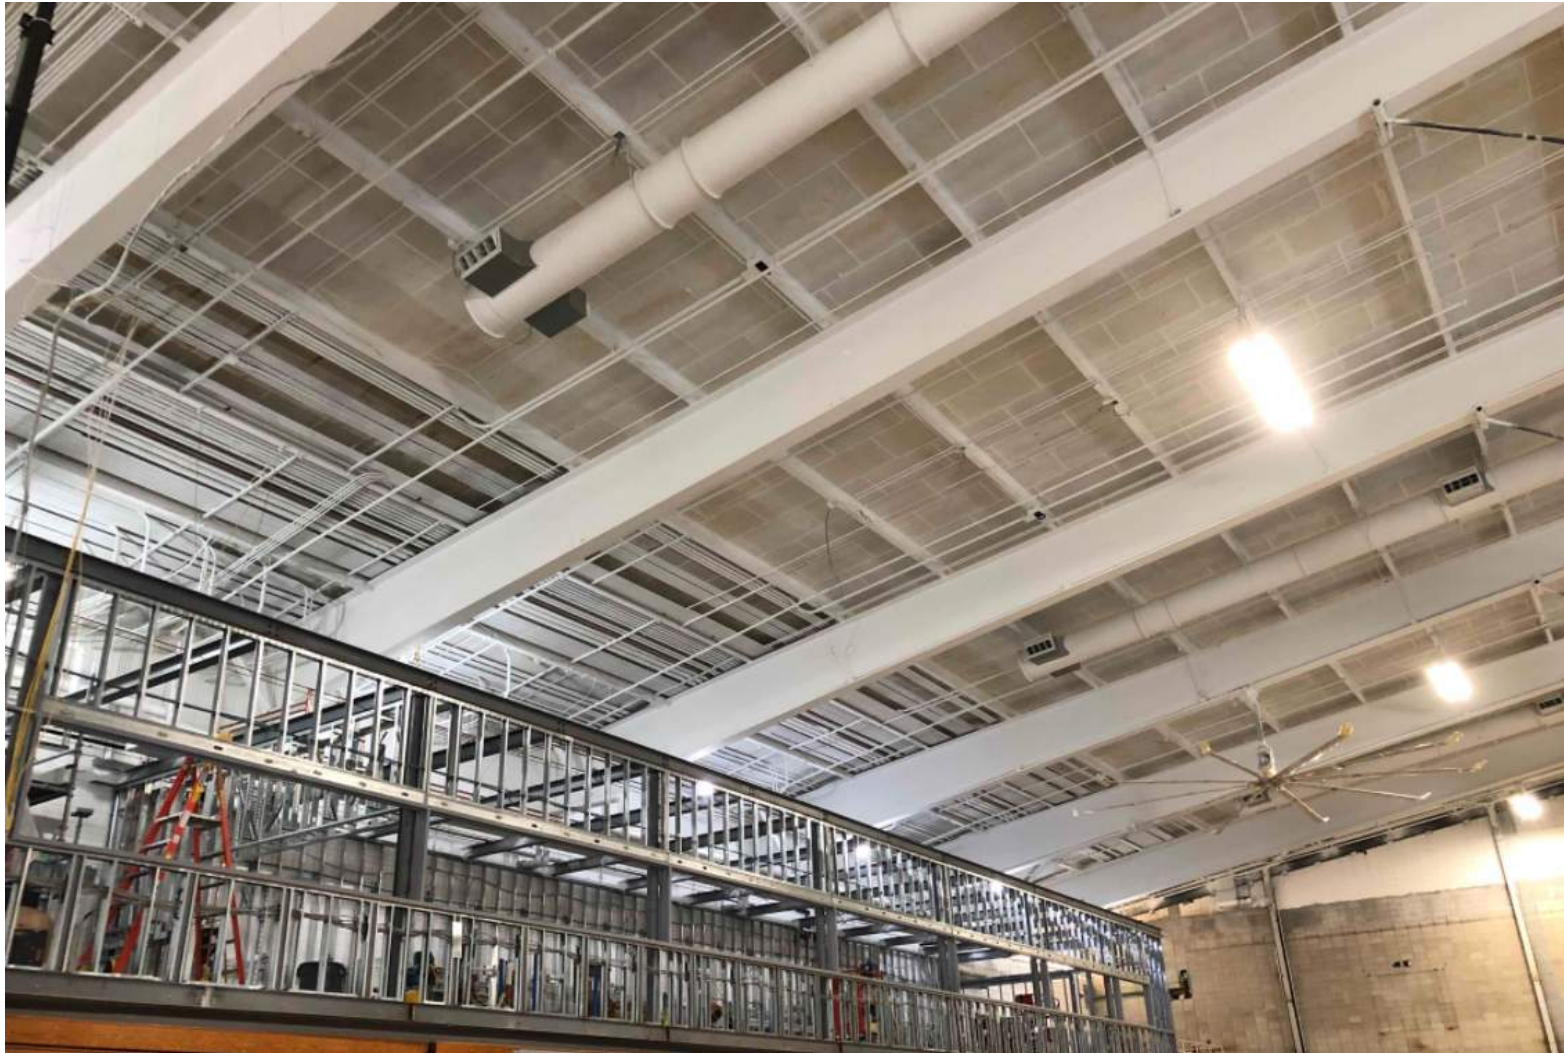

Progress Photos

- Area A, 1st Floor, administration area finishes

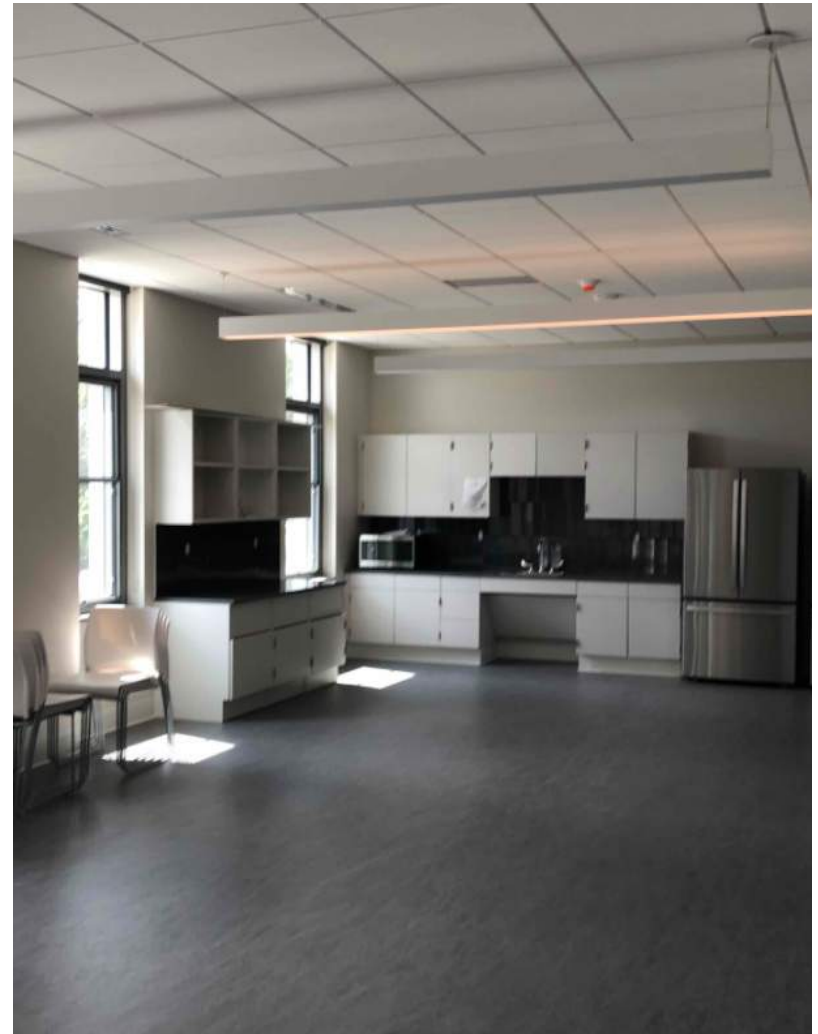

Progress Photos

- Area B Corridor finishes



- Area C Corridor wood veneer panels



Progress Photos – High School Main Entrance metal panel installation



Progress Photos

- Auditorium tiered seating installation



Progress Photos

- Installation of grating in Area C Mechanical Well



Progress Photos

- Sidewalk installation

