

# Belmont Middle & High School Project Update

October 2020



# Work Performed - October 2020

## **General**

- Continued Incorporating COVID-19 Provisions on Site for Safe Work Practices
- Completed MEP/Fire Protection Coordination Phase 1, Phase 2 ongoing
- Completed setting rooftop HVAC units

## **Civil/Site Work**

- Continued Construction of Permanent Roads

## **Building A**

- Completed Rough Installation of MEP/FP components
- Continued Installation of Masonry at Façade
- Continued drywall installation.
- Started glass installation after masonry
- Started interior wall finishes

## **Building B**

- Completed installation of window frames
- Completed spray fireproofing
- Completed installation of AVB
- Continued installation of MEP/FP rough-in
- Continued installation of masonry at façade
- Started installing catwalk in black box theater
- Started installing High School elevator

## **Building C**

- Completed under-slab utility installation
- Completed installation of exterior framing and sheathing
- Completed installation of roofing materials on main roof
- Continued concrete slab on grade placements
- Continued installation of AVB
- Continued installation of interior framing / early drywall
- Continued installation of MEP/FP components
- Continued renovation of pool area

# Look Ahead - November 2020

## **General**

- Continued Incorporating COVID-19 Provisions on Site for Safe Work Practices
- Complete temporary heat system

## **Building A**

- Complete installation of drywall
- Continue interior wall finishes
- Start painting walls
- Start installation of ceilings
- Start installation of tile

## **Building B**

- Continue installation of drywall
- Continue interior wall finishes
- Continue installing catwalk in auditorium and black box theater
- Continue installation of masonry at façade

## **Building C**

- Complete installation of AVB
- Complete installation of window frames
- Complete installation of slab on grade
- Continue renovation of pool
- Continue installation of curtain wall glass
- Continue framing interior walls
- Start installation of drywall

# Progress Photos

- Photo 1: Under-slab duct for pool drain ventilation



- Photo 2: Installation of vapor barrier and rebar in preparation of pouring slab on grade in area C






# Progress Photos

- Photo 3: First slab on grade pour of area C



- Photo 4: Installation of multi-story curtain wall at Area C South

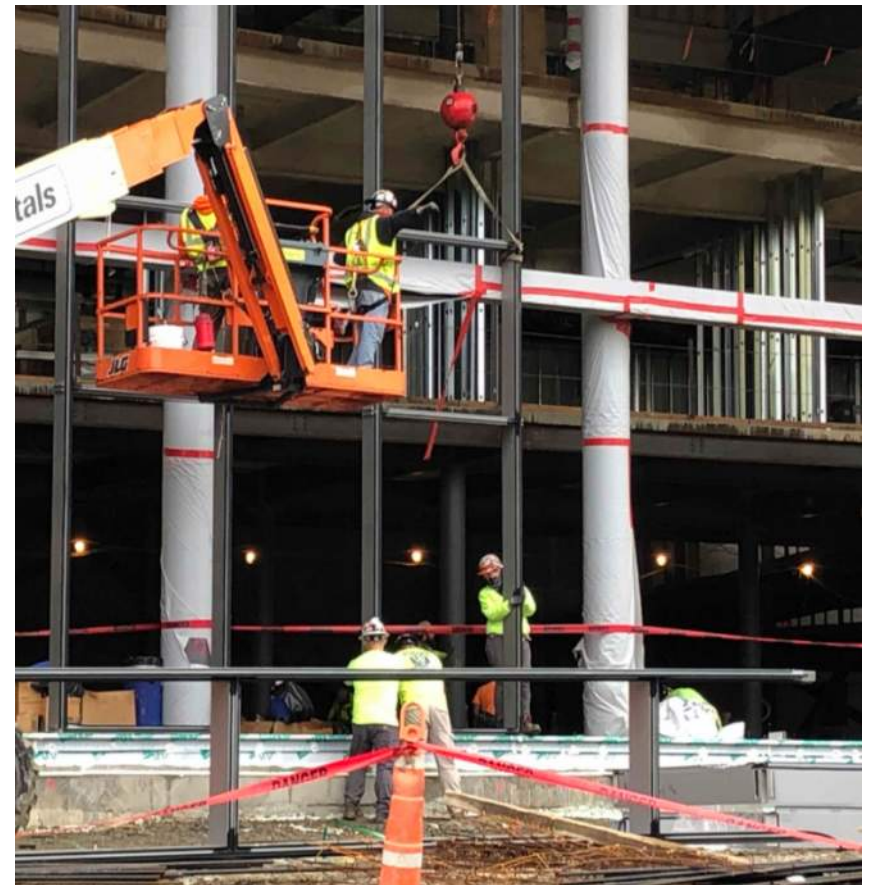

# Progress Photos

- Photo 5: Northwest elevation of Area B during installation of masonry and windows



- Photo 6: Installation of brick ties at south elevation of B Building





# Progress Photos

- Photo 7: Installation of masonry at west elevation of A building



# Progress Photos

- Photo 8: Setting HVAC rooftop units in area C mechanical well



- Photo 9: Area A, Level 2 interior finish ready for paint

