Activity ID	Activity Name	Remaining Duration	Start	Finish
Belmont Middle & High School - 10Sep20 Schedule Update				
Construction Summary				
SUM-3170	Abate & Restore Area at Locker Rooms	0	20-Dec-18 A	31-Dec-18 A
Phase 1 - Construct New School (Partial)				
SUM-3180	Bid & Award - Curtain Wall Design Assist	0	20-Mar-19 A	17-Jul-19 A
SUM-3160	Abate, Install Temp Structural for Phasing, Cut Cap, Demo Pool &	0	10-Jun-19 A	30-Aug-19 A
SUM-3130	Enabling Site Utilities & New Access Roadway	0	17-Jun-19 A	27-Aug-19 A
SUM-3140	Relocate Utilities at Building Footprint	0	08-Jul-19 A	15-Nov-19 A
SUM-3150	Mobilize Pile Operation & Perform Load Test	0	19-Aug-19 A	11-Sep-19 A
SUM-2000	Install Piles	0	27-Aug-19 A	26-Sep-19 A
SUM-3210	Substantial Completion of Early Bid Pacakge #2 Summer 2019 V	0		30-Aug-19 A
SUM- 2010	FRP Pile Caps & Grade Beams	0	16-Oct-19 A	24-Feb-20 A
SUM- 2020	Structural Steel Erection	0	15-Jan-20 A	15-May-20 A
SUM- 2030	Structural Steel Deck & Detailing	0	20-Jan-20 A	04-Jun-20 A
SUM- 2110	Install Final Site Utilities & Geothermal Wells	0	03-Feb-20 A	10-Sep-20
SUM- 2140	Prep & Place Slabs on Deck	0	18-Mar-20 A	08-Jul-20 A
SUM-3190	Shop Drawings Approved - Curtain Wall	0		20-Mar-20 A
SUM- 2150	Layout & Install Top Track	28	28-Apr-20 A	20-Oct-20
SUM- 2090	Underslab Utilities / Structural SOG	25	18-May-20 A	15-Oct-20
SUM- 2160	Spray Fireproof Steel	32	18-May-20 A	26-Oct-20
SUM- 2040	Frame Exterior Walls	45	01-Jun-20 A	13-Nov-20
SUM- 2070	Overhead MEP Installation	97	02-Jun-20 A	29-Jan-21
SUM-1010	Summer Renovations 2020	0	18-Jun-20 A	26-Aug-20 A
SUM- 2170	Sheath Exterior Walls	61	24-Jun-20 A	08-Dec-20
SUM- 2180	AVB Exterior Walls	72	26-Jun-20 A	23-Dec-20
SUM- 2050	Install Roof Sheating & AVB	114	08-Jul-20 A	24-Feb-21
SUM-3200	Begin - Curtain Wall	0	20-Jul-20 A	
SUM- 2210	Install Curtain Wall	138	20-Jul-20 A	30-Mar-21
SUM- 2190	Install Brick	106	03-Aug-20 A	11-Feb-21
SUM- 2130	Install Final Site Work	213	08-Sep-20 A	16-Jul-21
MILE- 2070	Building Tight - Area A	0		25-Sep-20
SUM- 2080	Install Drywall & Finishes	194	28-Sep-20	07-Jul-21
MILE- 2080	Building Tight - Area B	0		19-Oct-20
SUM- 2200	Install Metal Panels	78	29-Dec-20	20-Apr-21
MILE- 2090	Building Tight - Area CD	0		01-Feb-21
MILE-2080	Begin Equipment Start-up	0	11-Mar-21	
SUM- 2120	Install Playing Field (North End of Site)	49	12-Apr-21	21-Jun-21
SUM-3230	Summer Renovations 2021	51	24-Jun-21	03-Sep-21
MILE-2090	Receive Temporary Certificate of Occupancy for HIgh School	0		18-Aug-21
SUM-2135	Students / Staff Occupy New School	8	19-Aug-21	30-Aug-21
SUM- 2100	Install Playing Field (Western End of Site)	34	01-Sep-21	20-Oct-21
Phase 2 - Demo Remaining School / Complete School				
SUM-3000	Mobilize for Phase 2 Construction	13	28-Jun-21	15-Jul-21
SUM-3010	Complete Abatement & Demo of Existing Building	180	16-Jul-21	04-Apr-22
SUM-3030	Pile Installation	20	16-Dec-21	14-Jan-22
SUM-3040	Concrete Foundations	45	17-Jan-22	21-Mar-22
SUM-3050	Structural Steel Erection	40	29-Mar-22	24-May-22
SUM-3060	Install Decking / Detail	58	06-Apr-22	28-Jun-22
SUM-3220	Prep & Place Slabs on Deck	43	05-May-22	06-Jul-22
SUM-3070	Exterior Facade	173	09-Jun-22	15-Feb-23
SUM-3080	Overhead MEP Installation	109	22-Jul-22	28-Dec-22
MILE-3300	Building Tight - Area D	0		13-Sep-22
SUM-3090	Interior Drywall & Finishes	192	17-Oct-22	21-Jul-23
MILE-3320	Building Tight - Area F	0		07-Nov-22
MILE-3310	Receive Certificate Of Occupancy	0		21-Jul-23

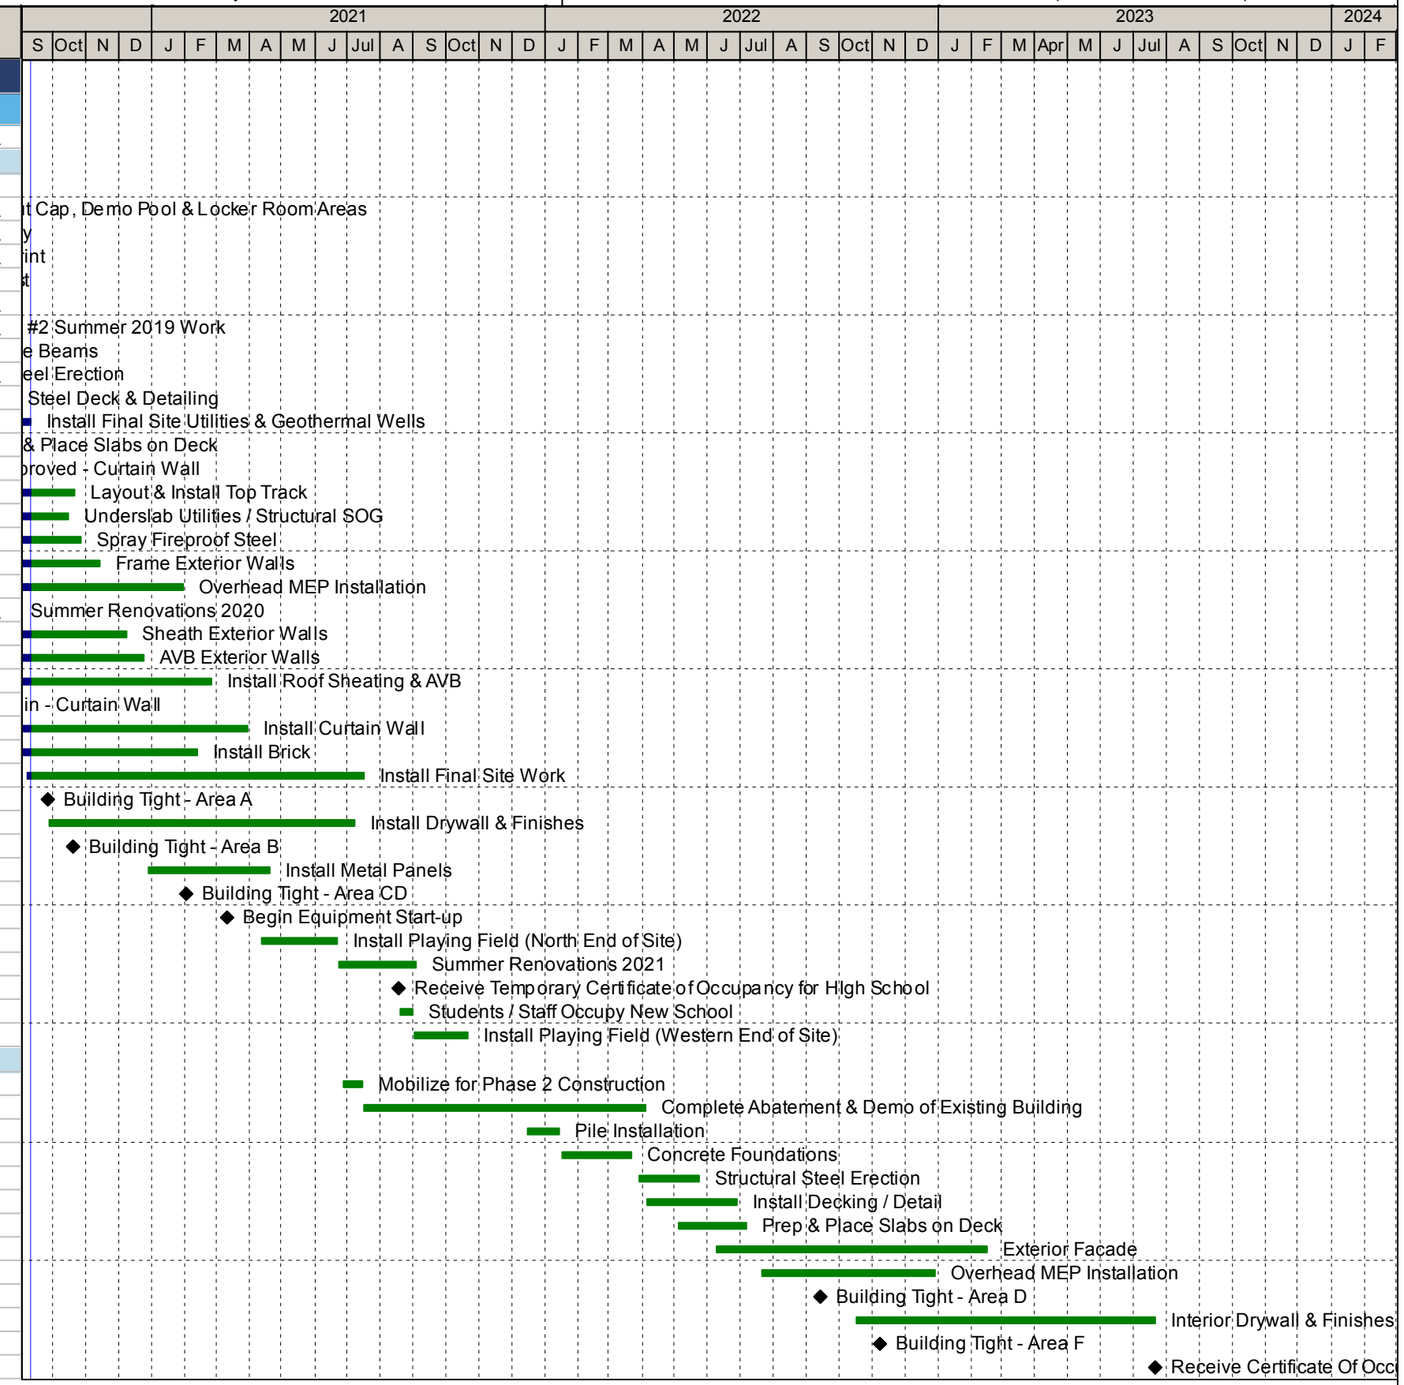

Remaining Level of Effort | Remaining Work
Actual Level of Effort | Critical Remaining Work
Actual Work | ◆ Milestone

TASK filter: Summary.

© Oracle Corporation

SKANSKA
